


Contract Time Estimate

Rd: SL 12
CSJ: 0581-02-151

County: DALLAS
Project: C 581-2-151

TASK #	Description	Quantity	Unit	Daily Rate	Duration	Pred Task	% Comp	Pred Task	% Comp	Pred Task	% Comp	Start Day	Finish Day
1	Initial TCP/Mobility	1	LS	0.2	5							1	5
2	Full Depth Concrete Repair	3,189	SY	90	36	1	100					6	41
3	Flex. Pvmnt. Repair/Shoulders	1,613	SY	70	24	2	50					24	47
4	Joint Repair	1,975	LF	158	13	3	50					36	48
5	Mill / Plane HMA	171,123	SY	4000	43	4	100					49	91
6	Inlay SMA	21,177	TON	495	43	4	100					49	91
7	Permanent Pavement Markings	67,626	LF	7000	10	5	100					92	101
8	Project Clean up	1	LS	0.2	5	7	100					102	106
9													
10													
11													
12													
13													
14													
15													
16													
17													
18													
19													
20													
21													
22													
23													
24													
25													
26													
27													
28													
29													
30													
31													
32													

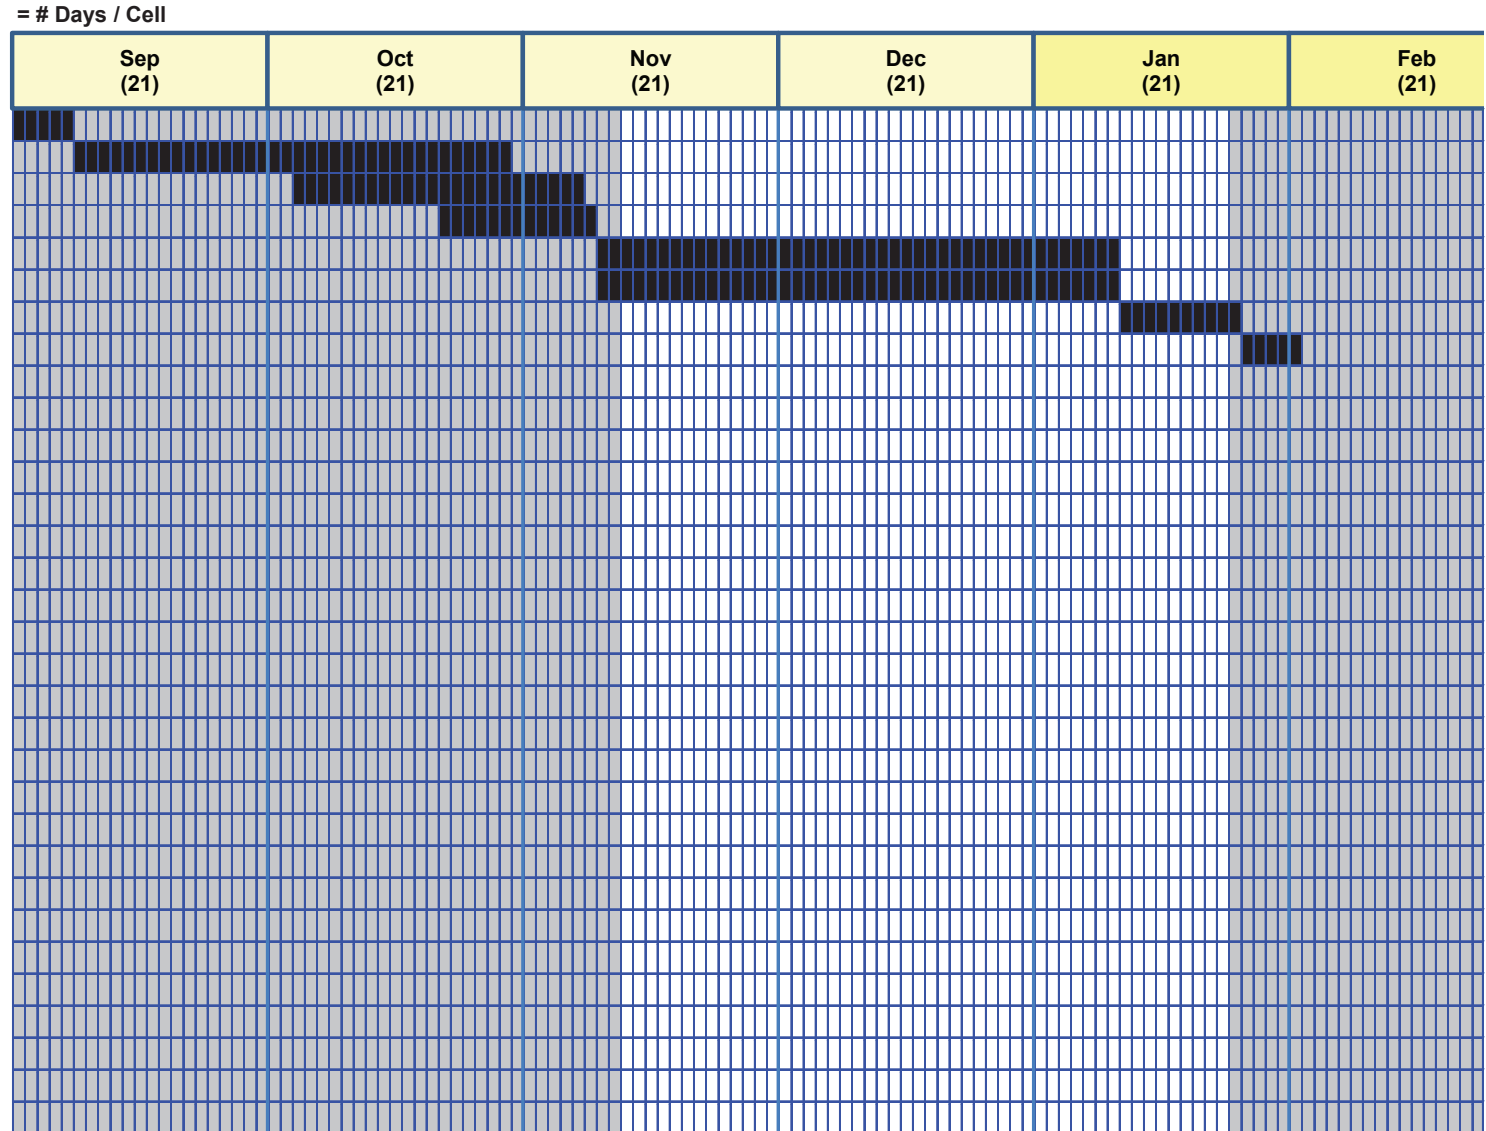

Construction Begin date: 9/1/2021
Construction End date: 4/1/2022

Number of Working Days: = 106
Total Number of Working Days 106*1.00 = 106
A Standard Work Week
Number of Months for Barricades: $\frac{106 * 1.22}{21} = 7.0$

DocuSigned by:
Chaitou Bah

4/27/2021

Signature

Date
