



**POLK COUNTY OFF-SYSTEM BRIDGE**  
 Texas Department of Transportation, Lufkin District  
 Kelly Rd at Bluff Creek  
 CSJ: 0911-04-089

#	Activity Name	Rate	Quantity	Duration	Start	Finish
1	<b>POLK COUNTY BRIDGE</b>			205	04-May-22	31-Mar-23
2	<b>POLK COUNTY BRIDGE REPLACEMENT</b>			153	04-May-22	05-Oct-22
3	PROJECT LETTING			0	04-May-22*	
4	NOTICE TO PROCEED			0	05-Jul-22*	
5	BEAM FABRICATION			90	06-Jul-22	05-Oct-22
6	<b>CONSTRUCTION TIME (WORKING DAYS)</b>			52	17-Oct-22	31-Mar-23
7	0911-04-089 - KELLY ROAD AT BLUFF CREEK			52	17-Oct-22	31-Mar-23
8	INSTALL TCP/DET/OUR	1 L/SDAY	1 LS	1	17-Oct-22	17-Oct-22
9	CLOSE ROAD/BEGIN CONSTRUCTION			0	18-Oct-22	
10	INSTALL SWP3	1 L/SDAY	1 LS	1	18-Oct-22	18-Oct-22
11	PREP ROW	2 STADAY	3.75 STA	2	19-Oct-22	20-Oct-22
12	REMOVE EXIST BRIDGE	5 EADAY	1 EA	2	21-Oct-22	24-Oct-22
13	EXCAVATION	500 CYDAY	190 CY	1	25-Oct-22	25-Oct-22
14	EMBANKMENT	500 CYDAY	595 CY	2	25-Oct-22	26-Oct-22
15	PLACE SRB & TEMP SEEDING	2000 SYDAY	1265 SY	1	27-Oct-22	27-Oct-22
16	CONSTRUCT DRILLED SHAFTS + 7 DAYS CURE	30 L/FDAY	300 LF	10	28-Oct-22	10-Nov-22
17	CONSTRUCT ABUTMENTS & WING WALLS + 7 DAYS CURE	2 EADAY	2 EA	10	30-Nov-22	04-Jan-23
18	CEMENT STABILIZED BACKFILL	45 CYDAY	81 CY	2	16-Jan-23	17-Jan-23
19	PLACE STONE RIPRAP	150 CYDAY	304 CY	2	30-Jan-23	31-Jan-23
20	INSTALL CONCRETE BEAMS	6 EADAY	4 EA	1	01-Feb-23	01-Feb-23
21	POUR BRIDGE DECK + 7 DAYS CURE	250 S/FDAY	1950 SF	8	21-Feb-23	02-Mar-23
22	PLACE FLEX BASE	400 SYDAY	775 SY	2	09-Mar-23	10-Mar-23
23	INSTALL T63 1LS, MBGF, SGT, & DAT	75 L/FDAY	325 LF	5	13-Mar-23	29-Mar-23
24	INSTALL OBJECT MARKERS & DELINEATORS	1 L/SDAY	1 LS	1	29-Mar-23	29-Mar-23
25	OPEN ROAD/END CONSTRUCTION			0	29-Mar-23	
26	SEEDING	2000 SYDAY	1265 SY	1	30-Mar-23	30-Mar-23
27	REMOVE SWP3/FINAL CLEANUP	1 L/SDAY	1 LS	1	31-Mar-23	31-Mar-23

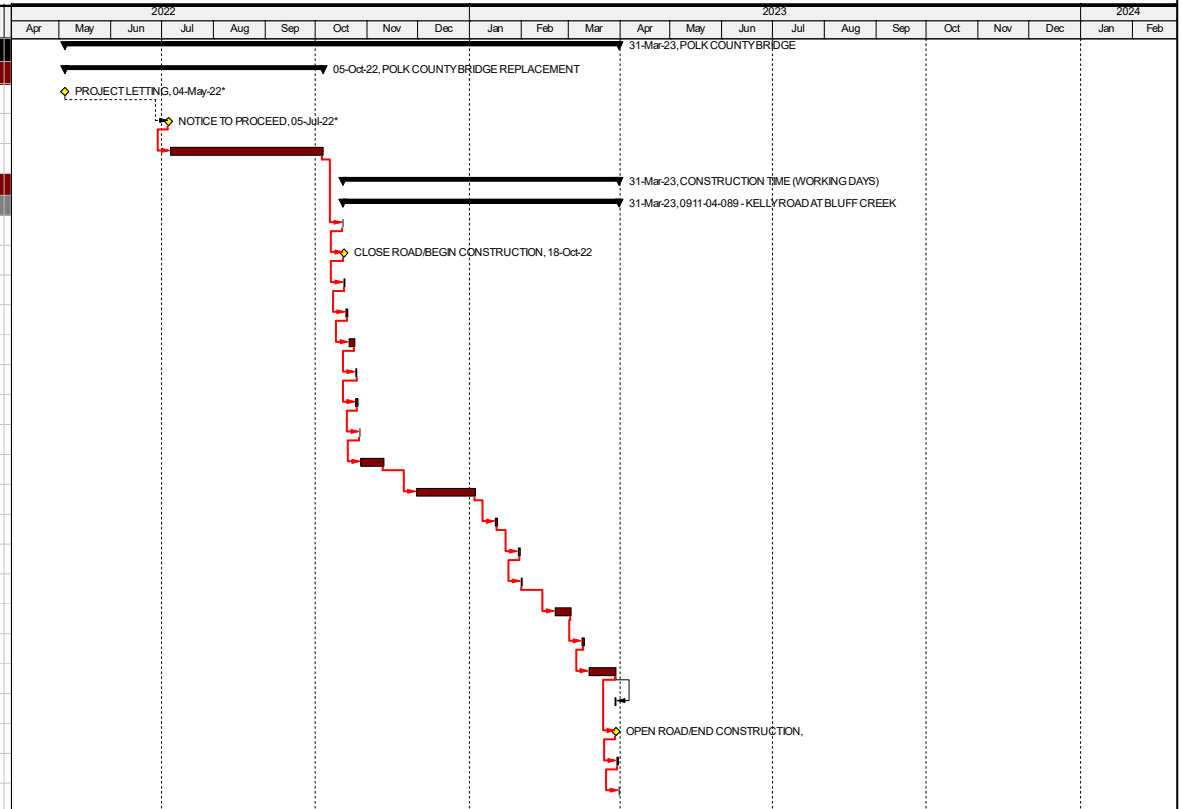

Project Letting: 04-May-2022  
 Construction Start Date: 17-Oct-2022  
 Construction End Date: 31-Mar-2023

Civil Consulting Group, PLLC for TxDOT Lufkin District  
 Based on: LFK Standard Workweek  
 Total Working Days: 52  
 Total Barricade Months: 6

*Trevor L. Castilla*  
 February 24, 2022
