



SHELBY COUNTY OFF-SYSTEM BRIDGE
 Texas Department of Transportation, Lufkin District
 CR 4123 at Bear Bayou
 CSJ: 0911-39-063

#	Activity Name	Rate	Quantity	Duration	Start	Finish
1	SHELBY COUNTY BRIDGE			200	04-May-22	09-Mar-23
2	SHELBY COUNTY BRIDGE REPLACEMENT			152	04-May-22	06-Oct-22
3	PROJECT LETTING			0	04-May-22*	
4	NOTICE TO PROCEED			0	05-Jul-22*	
5	BEAM FABRICATION			90	06-Jul-22	06-Oct-22
6	CONSTRUCTION TIME (WORKING DAYS)			48	17-Oct-22	09-Mar-23
7	0911-39-063 - CR 4123 AT BEAR BAYOU			48	17-Oct-22	09-Mar-23
8	INSTALL TCP/DETOUR	1 L/SDAY	1 LS	1	17-Oct-22	17-Oct-22
9	CLOSE ROAD/BEGIN CONSTRUCTION			0	18-Oct-22	
10	INSTALL SWP3	1 L/SDAY	1 LS	1	18-Oct-22	18-Oct-22
11	PREP ROW	2 STADAY	3.55 STA	2	19-Oct-22	20-Oct-22
12	REMOVE EXIST BRIDGE	5 EADAY	1 EA	2	21-Oct-22	24-Oct-22
13	EXCAVATION	500 CYDAY	300 CY	1	25-Oct-22	25-Oct-22
14	EMBANKMENT	500 CYDAY	296 CY	1	26-Oct-22	26-Oct-22
15	PLACE SRB & TEMP SEEDING	2000 SYDAY	1013 SY	1	27-Oct-22	27-Oct-22
16	CONSTRUCT DRILLED SHAFTS + 7 DAYS CURE	30 L/DFDAY	150 LF	5	28-Oct-22	03-Nov-22
17	CONSTRUCT ABUTMENTS & WING WALLS + 7 DAYS CURE	2 EADAY	2 EA	10	21-Nov-22	06-Dec-22
18	CEMENT STABILIZED BACKFILL	45 CYDAY	65.3 CY	2	28-Dec-22	29-Dec-22
19	PLACE STONE RIPRAP	120 CYDAY	269 CY	3	30-Dec-22	04-Jan-23
20	INSTALL CONCRETE BEAMS	6 EADAY	6 EA	1	26-Jan-23	26-Jan-23
21	POUR BRIDGE DECK + 7 DAYS CURE	250 SF/DAY	1962 SF	8	27-Jan-23	07-Feb-23
22	PLACE FLEX BASE	350 SY/DAY	667 SY	2	24-Feb-23	27-Feb-23
23	INSTALL T&S ILS, MBGF, SGT, & DAT	75 L/DFDAY	337.5 LF	5	28-Feb-23	06-Mar-23
24	INSTALL OBJECT MARKERS & DELINEATORS	1 L/SDAY	1 LS	1	06-Mar-23	06-Mar-23
25	OPEN ROAD/END CONSTRUCTION			0		06-Mar-23
26	INSTALL FENCE	200 L/DFDAY	203 LF	1	07-Mar-23	07-Mar-23
27	SEEDING	2000 SY/DAY	1097 SY	1	08-Mar-23	08-Mar-23
28	REMOVE SWP3/FINAL CLEANUP	1 L/SDAY	1 LS	1	09-Mar-23	09-Mar-23

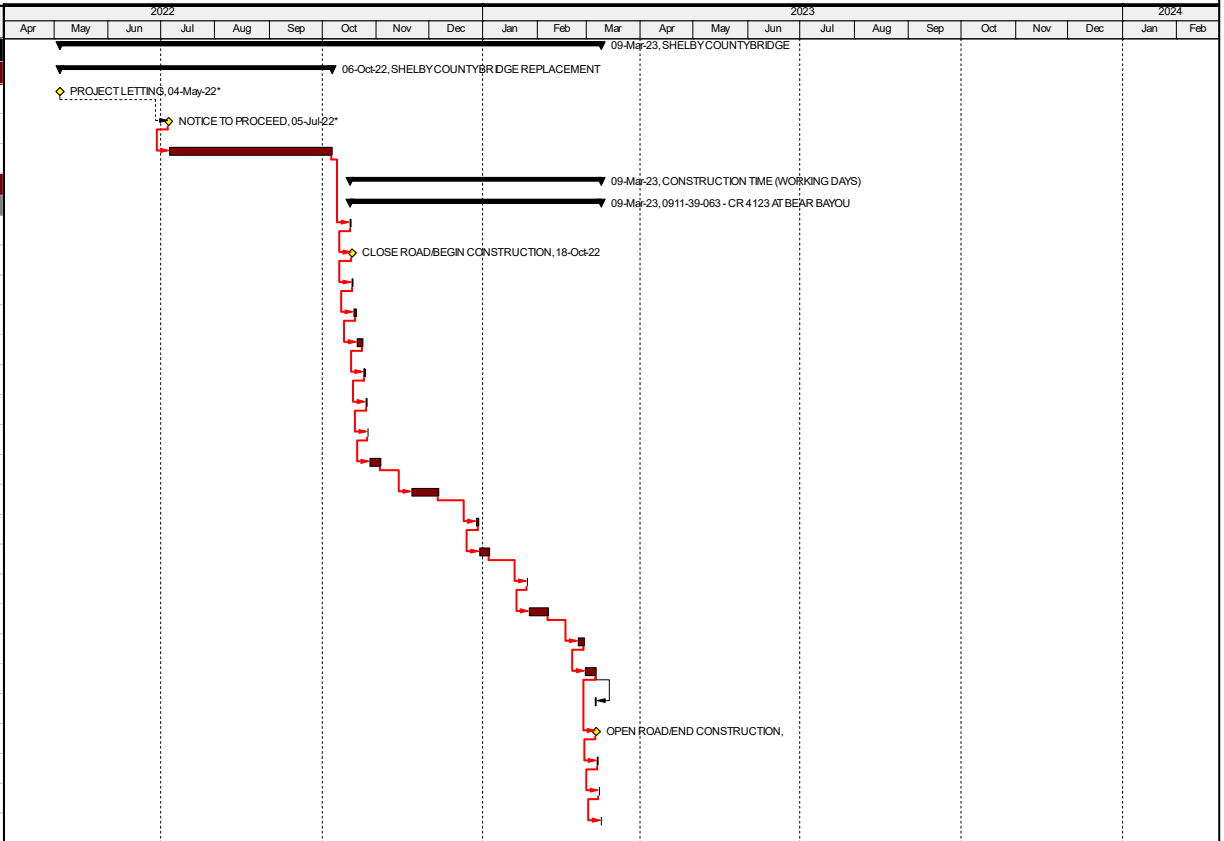

Project Letting: 04-May-2022
 Construction Start Date: 17-Oct-2022
 Construction End Date: 09-Mar-2023

Civil Consulting Group, PLLC for TxDOT Lufkin District
 Based on: LFK Standard Workweek
 Total Working Days: 48
 Total Barricade Months: 6

Trevor L. Castilla
 February 24, 2022
