


#	Activity ID	Activity Name	Quantity	Unit of Measure	Production Rate	Original Duration	Start	Finish	Calendar	2021												2022					
										Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr					
1	FM 770 CSJ 1096-01-065		80117		10617.00	128	Jun-04-21	Feb-18-22	Standard-15 Working Days/MO																		
2	CONSTRUCTION		80117		10617.00	128	Jun-04-21	Feb-18-22	Standard-15 Working Days/MO																		
3	TCP		6		3.00	128	Jun-04-21	Feb-18-22	Standard-15 Working Days/MO																		
4	TCP-1000	MOBILIZATION	4	LS	1.00	4	Jun-04-21	Jun-09-21	Standard-15 Working Days/MO																		
5	TCP-1010	SET ADVANCE WARNING SIGNS	1	LS	1.00	1	Jun-10-21	Jun-10-21	Standard-15 Working Days/MO																		
6	TCP-1020	FINAL CLEANUP	1	LS	1.00	1	Feb-18-22	Feb-18-22	Standard-15 Working Days/MO																		
7	EARTHWORK		31779		4500.00	120	Jun-16-21	Feb-15-22	Standard-15 Working Days/MO																		
8	EW-1000	EXCAVATION	5285	CY	500.00	11	Jun-16-21	Jul-07-21	Standard-15 Working Days/MO																		
9	EW-1010	EMBANKMENT	2642	CY	500.00	6	Jul-09-21	Jul-19-21	Standard-15 Working Days/MO																		
10	EW-1020	SEEDING	23852	SY	3500.00	7	Feb-02-22	Feb-15-22	Standard-15 Working Days/MO																		
11	DRAINAGE		1240		212.00	34	Oct-04-21	Dec-14-21	Standard-15 Working Days/MO																		
12	DRG-1000	REMOVE DRIVEWAY/INTERSECTION STR PIPE	490	LF	100.00	5	Oct-04-21	Oct-13-21	Standard-15 Working Days/MO																		
13	DRG-1010	INSTALL DRIVEWAY/INTERSECTION CULVERT	496	LF	100.00	5	Oct-15-21	Oct-25-21	Standard-15 Working Days/MO																		
14	DRG-1020	INSTALL DRIVEWAY/INTERSECTION SET	254	EA	12.00	22	Oct-28-21	Dec-14-21	Standard-15 Working Days/MO																		
15	ROADWAY		47090		5900.00	96	Jul-21-21	Feb-01-22	Standard-15 Working Days/MO																		
16	RDWY-1000	PRIME COAT	29969	GAL	4500.00	7	Jul-21-21	Aug-03-21	Standard-15 Working Days/MO																		
17	RDWY-1010	HMA	10466	TON	350.00	30	Aug-04-21	Oct-01-21	Standard-15 Working Days/MO																		
18	RDWY-1020	ACP DRIVEWAYS/INTERSECTION	1758	SY	300.00	6	Dec-15-21	Dec-24-21	Standard-15 Working Days/MO																		
19	RDWY-1030	CONC DRIVEWAYS	99	SY	300.00	1	Dec-28-21	Dec-28-21	Standard-15 Working Days/MO																		
20	RDWY-1040	BASE DRIVEWAYS	4527	SY	300.00	16	Dec-30-21	Jan-28-22	Standard-15 Working Days/MO																		
21	RDWY-1050	ACP TURNOUTS	271	SY	150.00	2	Jan-31-22	Feb-01-22	Standard-15 Working Days/MO																		
22	EROSION CONTROL		1		1.00	1	Jun-14-21	Jun-14-21	Standard-15 Working Days/MO																		
23	ERO-1000	SET EROSION CONTROL DEVICES	1	LS	1.00	1	Jun-14-21	Jun-14-21	Standard-15 Working Days/MO																		
24	TRAFFIC/ITS		1		1.00	1	Feb-16-22	Feb-16-22	Standard-15 Working Days/MO																		
25	TRF-1000	PLACE FINAL STRIPING	1	LS	1.00	1	Feb-16-22	Feb-16-22	Standard-15 Working Days/MO																		



- █ Remaining Level of Effort
- █ Actual Level of Effort
- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone
- ▬ summary

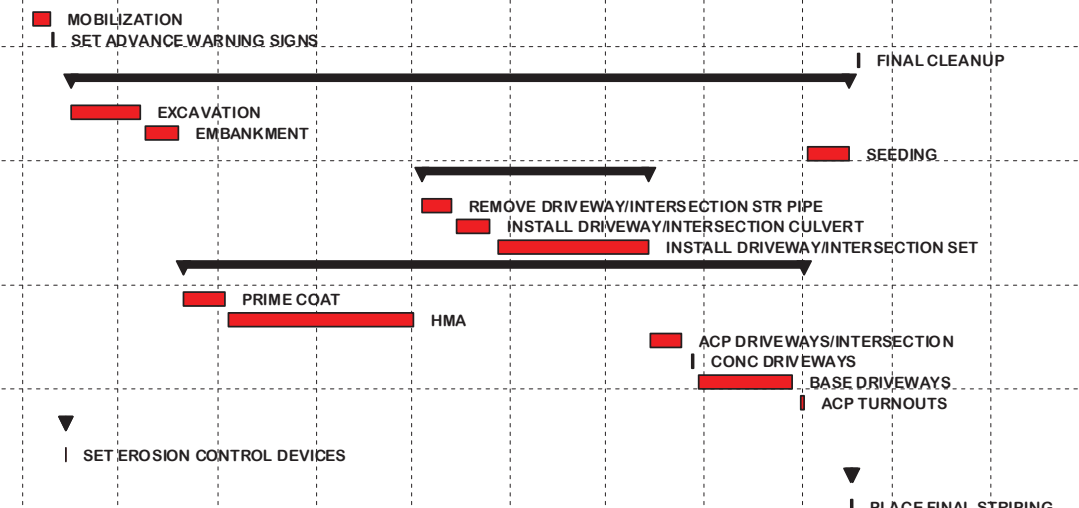

02/03/2021

Feb-03-21

This schedule assumes generic resources, production rates, sequences of construction and average weather conditions based on historic data. The Department will not adjust the number of working days and milestones, if any, due to differences in opinion regarding any assumptions made in the preparation of the schedule or for errors, omissions, or discrepancies found in the Department's conceptual time of determination schedule.

128 Working Days/ 15 working days per month = 9 months of Barricades, Signs, and Traffic Handling

Approximate Construction Start Date: June 04, 2021

Approximate Construction End Date: February 18, 2022
