

Contract Time Estimate

Rd: US 380, ETC.

County: WISE

INSERT
HIGHLIGHTED
OF ROWS



DELETE
HIGHLIGHTED
ROWS

CSJ: 6369-37-001

Project: RMC 6369-37-001

TASK #	Description	Quantity	Unit	Daily Rate	Duration	Pred Task	% Compl	Pred Task	% Compl	Pred Task	% Compl	Start Day	Finish Day
1	MOBILIZATION	1	EA	1	1		100					1	1
2	TY I W BRK 8" .60 MIL	2,119	LF	200000	1	1	100					2	2
3	TY I W SLD 8" .60 MIL	128,840	LF	200000	1	2	100					3	3
4	TY I Y SLD 4" PROF	92,630	LF	40000	3	3	100					4	6
5	TY I W SLD 4" PROF	169,500	LF	40000	5	4	100					7	11
6	TY I Y BRK 4" PROF	17,603	LF	40000	1	5	100					12	12
7	TY I W BRK 4" .60 MIL	190,276	LF	200000	1	6	100					13	13
8	TY I W SLD 4" .60 MIL	1,519,374	LF	200000	8	7	100					14	21
9	TY I W SLD 4" .90 MIL	4,000	LF	200000	1	8	100					22	22
10	TY I Y BRK 4" .60 MIL	101,594	LF	200000	1	9	100					23	23
11	TY I Y SLD 4" .60 MIL	1,213,099	LF	200000	7	10	100					24	30
12	TY I Y SLD 4" .90 MIL	4,000	LF	200000	1	11	100					31	31
13	PR FB MRK W 24"	2,449	LF	1500	2	12	100					32	33
14	PR FB MRK W AAROW	43	EA	20	3	13	100					34	36
15	PR FB MRK W WORD	36	EA	20	2	14	100					37	38
16	PR FB MRK 36" TRI	270	EA	50	6	15	100					39	44
17	RPM TY I-C	1,488	EA	2000	1	16	100					45	45
18	RPM TY II-AA	21,208	EA	2000	11	17	100					46	56
19	RPM TY II-C-R	18,127	EA	2000	10	18	100					57	66
20	ELIM PV MRKS 4"	371,048	LF	60000	7	19	100					67	73
21	ELIM PV MRKS 12"	1,265	LF	1000	2	20	100					74	75
22	ELIM PV MARKS 24"	1,975	LF	1000	2	21	100					76	77
23	ELIM PV MRK AAROW	43	EA	20	3	22	100					78	80
24	ELIM PV MARK WORD	26	EA	20	2	23	100					81	82
25	ELIM PV MRK 36" TRI	279	EA	50	6	24	100					83	88
26													
27													

= # Days / Cell

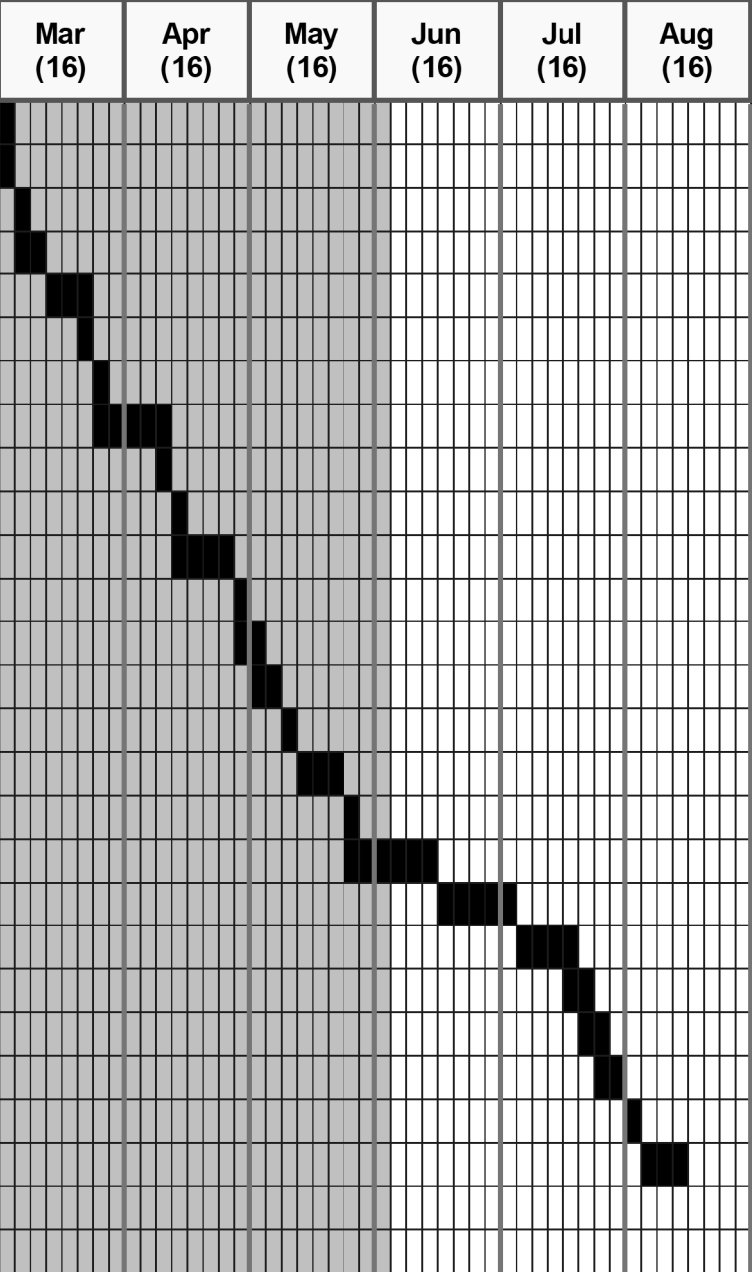

DocuSigned by:
Edrean Cheng, PE
1C2C4AEE88A847B...
9/23/2020
