


Contract Time Estimate

Rd: Various County: Harris
 CSJ: 0912-72-610 Project: _____

TASK #	Description	Quantity	Unit	Daily Rate	Duration	Pred Task	% Compl	Pred Task	% Compl	Pred Task	% Compl	Start Day	Finish Day
1	Authorization	1	LS	1	1							1	1
2	Mobilization	1	LS	1	1	1	100					2	2
3	SW3P Items	100	LF	100	1	2	100					3	3
4	Place Advanced Signs	1	DAY	0.2	5	3	100					4	8
5	Phase 1 Step 1												
6	TMA (Stationary)	11	DAY	1	11	4	100					9	19
7	TMA (Mobile Operation)	35	DAY	1	35	4	100					9	43
8	PCMS	25	DAY	1	25	4	100					9	33
9	Concrete Structure Repair	1.312	CY	0.05	27	4	100					9	35
10	Concrete Crack Repair	20	LF	2.8	8	9	100					36	43
11	Phase 1 Step 2												
12	TMA (Stationary)	11	DAY	1	11	10	100					44	54
13	TMA (Mobile Operation)	68	DAY	1	68	10	100					44	111
14	PCMS	50	DAY	1	50	10	100					44	93
15	Install Pedestrian Barrier	33,186	LF	500	67	10	100					44	110
16	Cleaning/Sweeping (Center Median)	1	CYC	1	1	15	100					111	111
17	Phase 2 Step 1												
18	TMA (Stationary)	9	DAY	1	9	16	100					112	120
19	TMA (Mobile Operation)	19	DAY	1	19	16	100					112	130
20	PCMS	10	DAY	1	10	16	100					112	121
21	Concrete Structure Repair	0.239	CY	0.05	5	16	100					112	116
22	Concrete Crack Repair	38	LF	2.8	14	21	100					117	130
23	Phase 2 Step 2												
24	TMA (Stationary)	9	DAY	1	9	22	100					131	139
25	TMA (Mobile Operation)	62	DAY	1	62	22	100					131	192
26	PCMS	45	DAY	1	45	22	100					131	175
27	Install Pedestrian Barrier	29,660	LF	500	60	22	100					131	190
28	Cleaning/Sweeping (Center Median)	1	CYC	1	1	27	100					191	191
29	Remove SWP3	100	LF	100	1	28	100					192	192
30													
31													
32	192 Working Days												
33	15 Working Days Per Month												
34	13 Months of Barricades												
35													
36	Start date: July 1, 2021												
37	End date: July 31, 2022												
38													
39													
40													
41													
42													

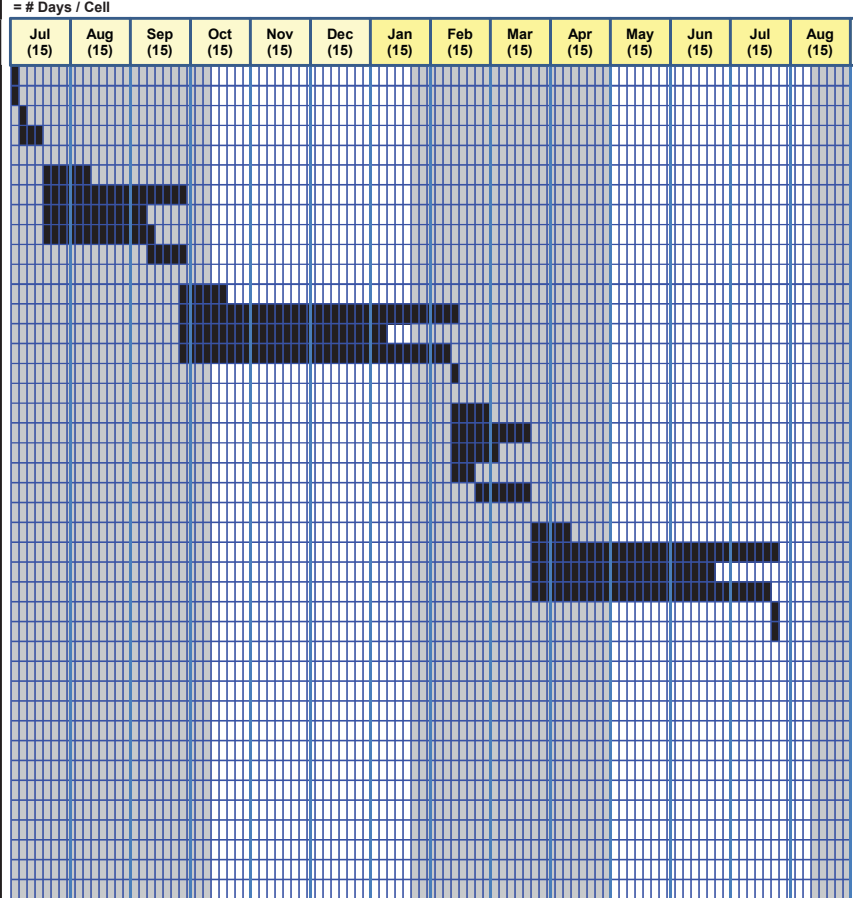

12/9/2020

DocuSigned by:
Alexine Stittiams-Ward, P.E.
 9D6BA739BD7743D...
