


ID	Task Name	Duration	Start	Finish	Predecessors
1	<b>US 83 South</b>	<b>1049 days</b>	<b>Mon 1/6/20</b>	<b>Mon 2/12/24</b>	
2	<b>Segment 1 &amp; 2</b>	<b>154 days</b>	<b>Mon 1/6/20</b>	<b>Fri 8/7/20</b>	
3	<b>Phase 1</b>	<b>25 days</b>	<b>Mon 1/6/20</b>	<b>Fri 2/7/20</b>	
4	Prep ROW	2 days	Mon 1/6/20	Tue 1/7/20	
5	Install SCF	1 day	Wed 1/8/20	Wed 1/8/20	4
6	Place PCTB	6 days	Wed 1/8/20	Wed 1/15/20	4
7	Extend SB Drainage	1 day	Thu 1/16/20	Thu 1/16/20	6
8	Construct Temp Drainage	1 day	Fri 1/17/20	Fri 1/17/20	7
9	Construct Wingwalls	8 days	Fri 1/17/20	Tue 1/28/20	7
10	Install Temp Shoring	1 day	Mon 1/20/20	Mon 1/20/20	8
11	Construct Temp Pvmt Base	11 days	Tue 1/21/20	Tue 2/4/20	10
12	Construct Temp Pvmt Aspht	7 days	Wed 1/29/20	Thu 2/6/20	11FS-5 days
13	Add Temp Pvmnt/PTB at Culverts	1 day	Fri 2/7/20	Fri 2/7/20	12
14	Install Temp Pvmnt Marking	1 day	Fri 2/7/20	Fri 2/7/20	12
15	<b>Phase 2</b>	<b>61 days</b>	<b>Mon 2/10/20</b>	<b>Mon 5/4/20</b>	<b>3</b>
16	Move PCTB	6 days	Mon 2/10/20	Mon 2/17/20	3
17	Extend NB Drainage	1 day	Tue 2/18/20	Tue 2/18/20	16
18	Construct Temp Drainage	1 day	Wed 2/19/20	Wed 2/19/20	17
19	Construct Wingwalls	8 days	Wed 2/19/20	Fri 2/28/20	17
20	Install Temp Shoring	1 day	Thu 2/20/20	Thu 2/20/20	18
21	Add Temp Pvmnt/PTB at Culverts	1 day	Fri 2/21/20	Fri 2/21/20	20
22	Remove Existing Base	11 days	Fri 2/21/20	Fri 3/6/20	20
23	Excavate Subgrade	1 day	Mon 3/9/20	Mon 3/9/20	22
24	Proof Roll	21 days	Tue 3/10/20	Tue 4/7/20	23
25	Lime Treat Subgrade	16 days	Mon 3/23/20	Mon 4/13/20	24FS-12 days
26	Place Cem Treat Base	16 days	Fri 3/27/20	Fri 4/17/20	25FS-12 days
27	Apply Prime Coat	2 days	Mon 4/20/20	Tue 4/21/20	26
28	Place Ty B Superpave	9 days	Tue 4/21/20	Fri 5/1/20	27FS-1 day
29	Install Temp Pvmnt Marking	1 day	Mon 5/4/20	Mon 5/4/20	28
30	<b>Phase 3</b>	<b>68 days</b>	<b>Tue 5/5/20</b>	<b>Fri 8/7/20</b>	<b>15</b>
31	Move PCTB	6 days	Tue 5/5/20	Tue 5/12/20	15
32	Remove Temp Pvmnt	9 days	Wed 5/13/20	Tue 5/26/20	31
33	Remove Existing Base	11 days	Wed 5/13/20	Thu 5/28/20	31
34	Excavate Subgrade	1 day	Fri 5/29/20	Fri 5/29/20	33
35	Proof Roll	21 days	Mon 6/1/20	Mon 6/29/20	34
36	Lime Treat Subgrade	16 days	Fri 6/12/20	Fri 7/3/20	35FS-12 days
37	Place Cem Treat Base	16 days	Thu 6/18/20	Thu 7/9/20	36FS-12 days
38	Apply Prime Coat	2 days	Fri 7/10/20	Mon 7/13/20	37

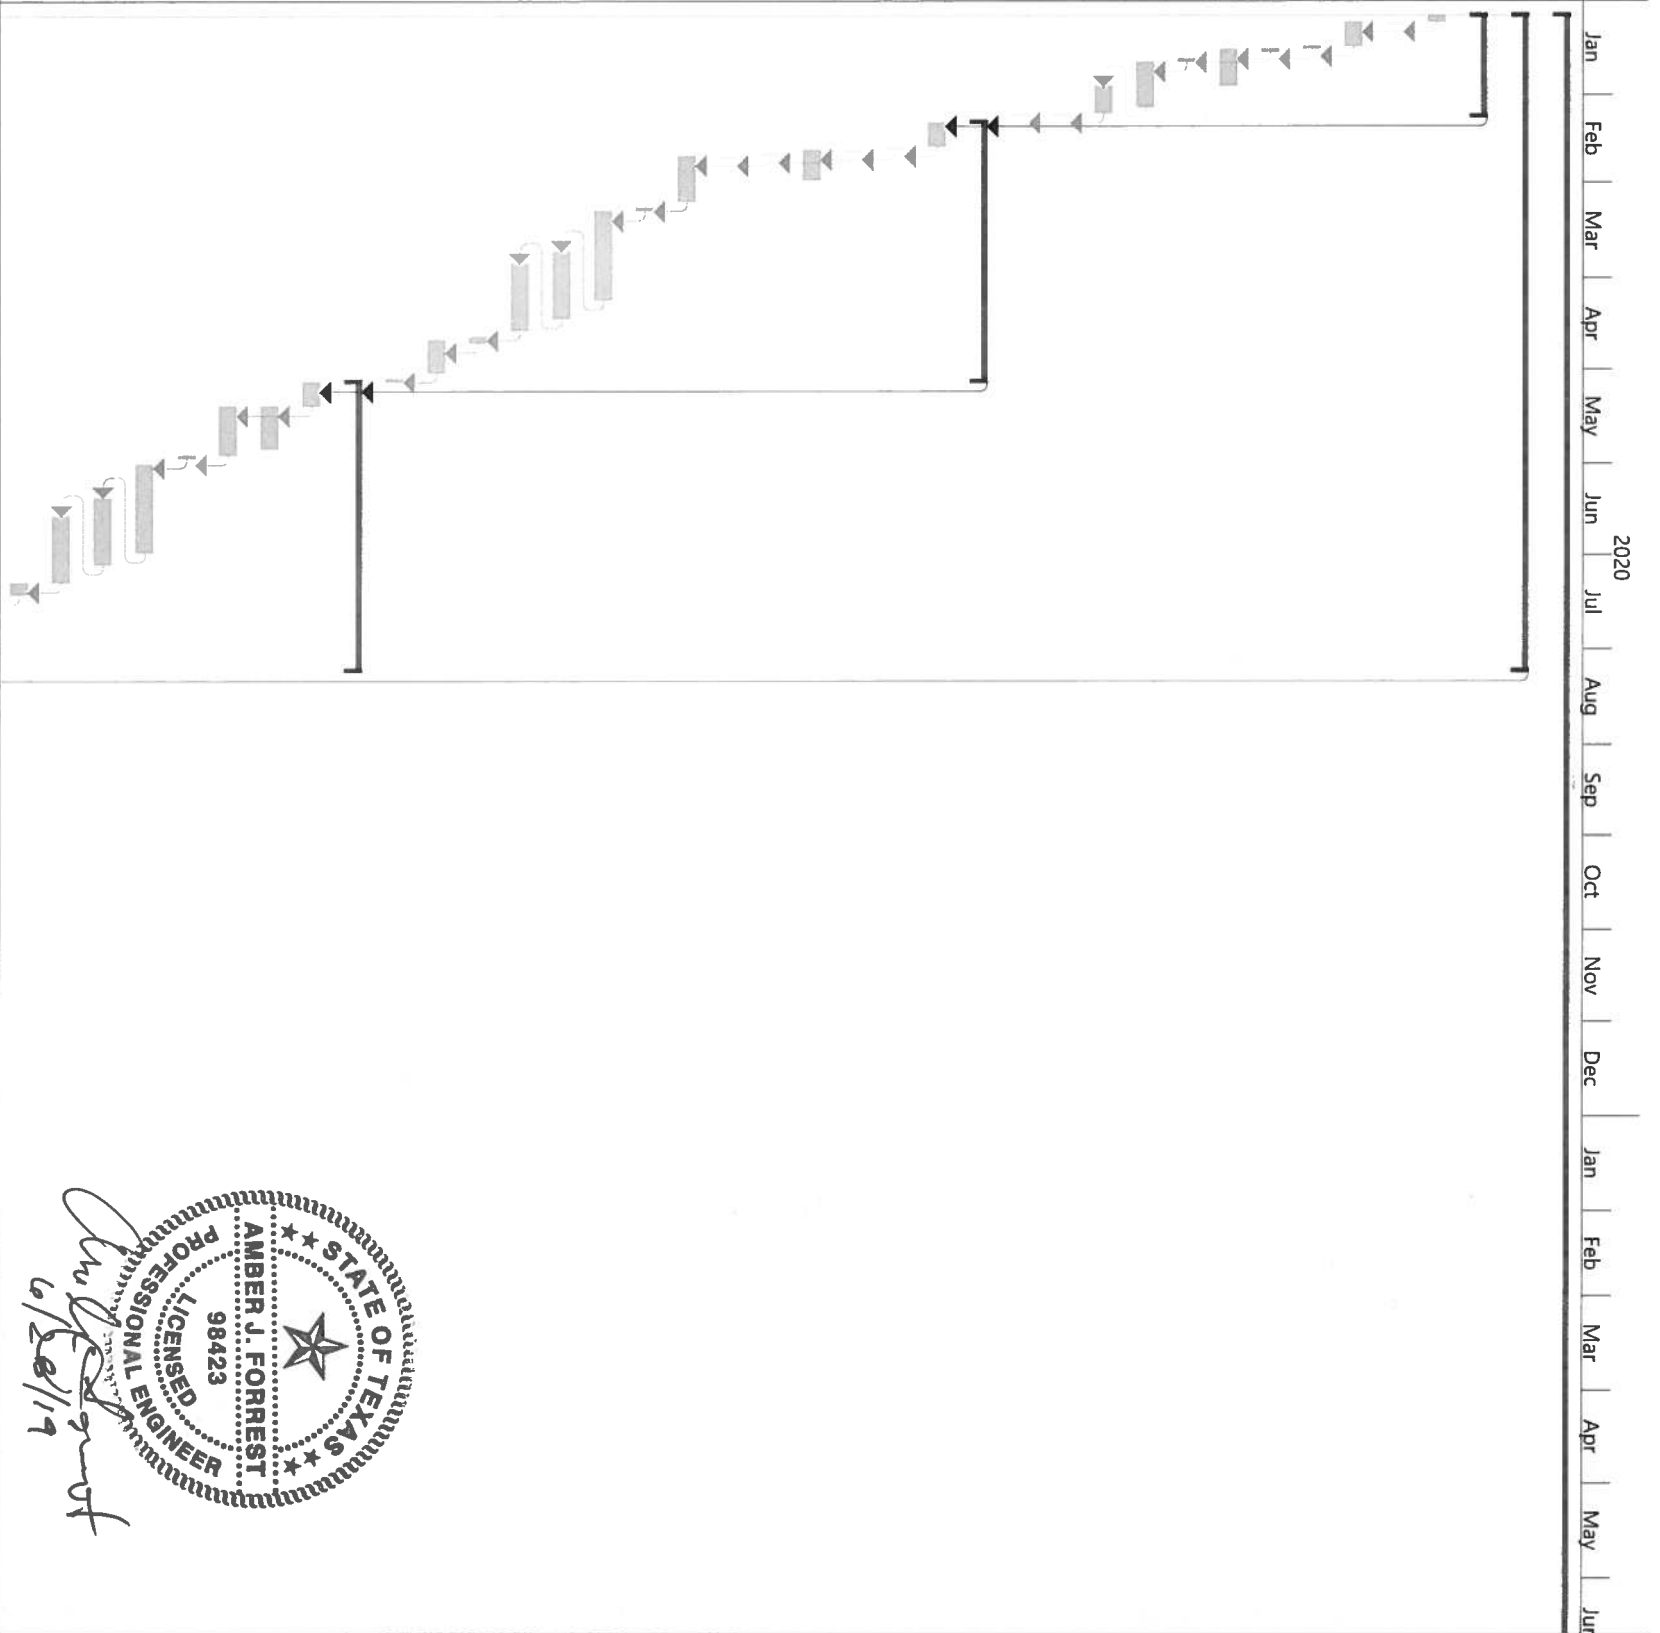

Project: US 83 037 Construction  
Date: Fri 6/28/19

Task Split Milestone Summary

Project Summary Inactive Task Inactive Milestone Inactive Summary

Manual Task Duration-only Manual Summary

Start-only Finish-only External Milestone

Deadline Progress Manual Progress



ID	Task Name	Duration	Start	Finish	Predecessors
39	Place Ty B Superpave	9 days	Mon 7/13/20	Thu 7/23/20	38FS-1 day
40	Remove Temp Drainage	1 day	Fri 7/24/20	Fri 7/24/20	39
41	Remove SCF	2 days	Mon 7/27/20	Tue 7/28/20	40
42	Apply Drill Seeding	8 days	Wed 7/29/20	Fri 8/7/20	41
43	Segment 3 & 4	119 days	Mon 8/10/20	Wed 1/27/21	2
84	Segment 5	124 days	Thu 1/28/21	Wed 7/21/21	43
125	Segment 6, 7, & 8	129 days	Thu 7/22/21	Mon 1/24/22	84
166	Segment 9, 10, & 11	161 days	Tue 1/25/22	Fri 9/9/22	125
207	Segment 12 & 13	124 days	Mon 9/12/22	Tue 3/7/23	166
248	Segment 14 & 15	106 days	Wed 3/8/23	Fri 8/4/23	207
289	Phase 4	88 days	Mon 8/7/23	Fri 12/8/23	248
290	Remove PCTB and CCA	6 days	Mon 8/7/23	Mon 8/14/23	248
291	Apply Trackless Tack	6 days	Tue 8/15/23	Tue 8/22/23	290
292	Place Ty C Surface Course	69 days	Thu 8/17/23	Wed 11/22/23	291FS-4 days
293	Install Permanent Striping	4 days	Fri 11/24/23	Wed 11/29/23	292
294	Apply Pavement Seal	3 days	Thu 11/30/23	Mon 12/4/23	293
295	Install Pavement Markers	4 days	Tue 12/5/23	Fri 12/8/23	294
296	WOE Segment 1	44 days	Mon 12/11/23	Mon 2/12/24	289
297	Phase 1	8 days	Mon 12/11/23	Wed 12/20/23	289
298	Prep ROW	1 day	Mon 12/11/23	Mon 12/11/23	289
299	Install SCF	7 days	Tue 12/12/23	Wed 12/20/23	298
300	Place PCTB	1 day	Tue 12/12/23	Tue 12/12/23	298
301	Construct Temp Pvmnt Base	2 days	Wed 12/13/23	Thu 12/14/23	300
302	Construct Temp Pvmnt Asph	1 day	Fri 12/15/23	Fri 12/15/23	301
303	Install Temp Pvmnt Marking	1 day	Mon 12/18/23	Mon 12/18/23	302
304	Phase 2	9 days	Thu 12/21/23	Thu 1/4/24	297
312	Phase 3	20 days	Fri 1/5/24	Thu 2/1/24	304
322	Phase 4	7 days	Fri 2/2/24	Mon 2/12/24	312
323	Remove PCTB and CCA	1 day	Fri 2/2/24	Fri 2/2/24	312
324	Apply Trackless Tack	1 day	Mon 2/5/24	Mon 2/5/24	323
325	Install Concrete Pavement	1 day	Mon 2/5/24	Mon 2/5/24	323
326	Place Ty C Surface Course	1 day	Tue 2/6/24	Tue 2/6/24	324
327	Construct Drill Shaft	1 day	Wed 2/7/24	Wed 2/7/24	326
328	Install Light Poles	3 days	Thu 2/8/24	Mon 2/12/24	327
329	Install Permanent Striping	1 day	Wed 2/7/24	Wed 2/7/24	326
330	Apply Pavement Seal	1 day	Thu 2/8/24	Thu 2/8/24	329



Project: US 83 037 Construction  
Date: Fri 6/28/19

Task Split Milestone Summary

Project Summary Inactive Task Inactive Milestone Inactive Summary

Manual Task Duration-only Manual Summary


Start-only Finish-only External Milestone

Deadline Progress Manual Progress

Project: US 83 037 Construction  
 Date: Fri 6/28/19

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	



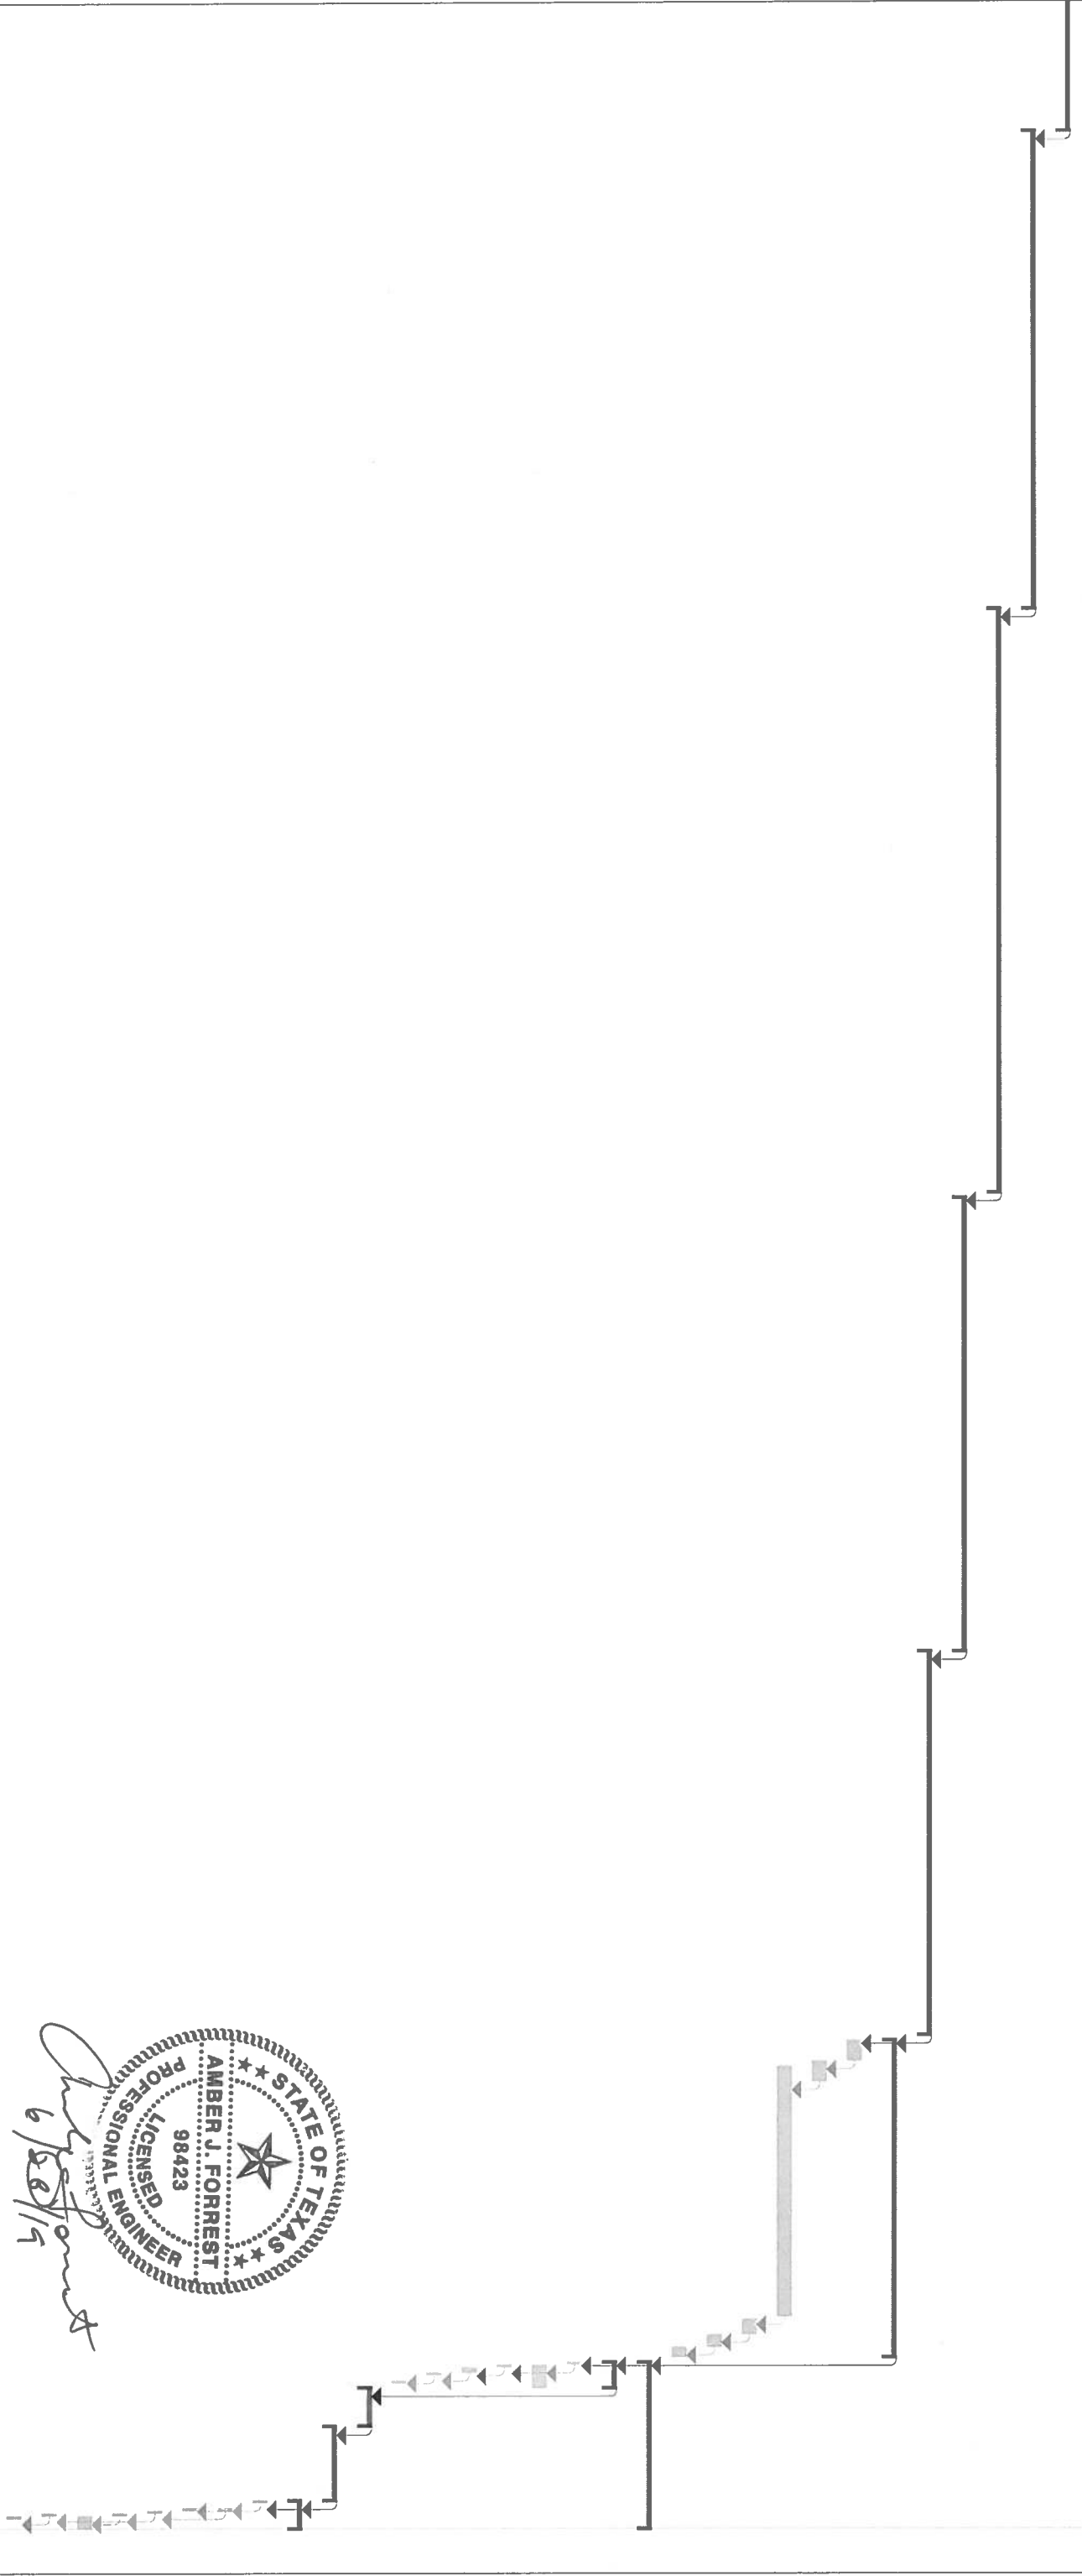

Project: US 83 037 Construction  
Date: Fri 6/28/19

Task	Project Summary	Manual Task	Start-only	Deadline
Split	.....	.....	.....	.....
Milestone	◆	◆	◆	◆
Summary	.....	.....	.....	.....
