

LAKE CASA BLANCA


County: WEBB

0922-33-206


Project: C 922-33-206

Description	Quantity	Unit	Daily Rate	Duration	Pred Task	% Comp	Pred Task	% Comp	Pred Task	% Comp	Start Day	Finish Day	= # Days / Cell				
													Sep (20)	Oct (20)	Nov (20)	Dec (20)	Jan (20)
<b>CSJ: 0922-33-206</b>	<b>89</b>	<b>DAYS</b>	<b>1</b>	<b>89</b>							1	89					
<b>LOC.3 - (BATH HOUSE)</b>	<b>12</b>	<b>DAYS</b>	<b>1</b>	<b>12</b>							1	12					
Mobilization	1	EA	2	1		100					1	1					
Setting Barricades	1	EA	2	1	4	100					2	2					
Place Traffic Control	1	EA	2	1	5	100					3	3					
Remove Material	4,796	SY	5000	1	6	100					4	4					
Flex Base Repair	4,796	SY	1500	4	7	100					5	8					
Prime Coat	959	GAL	4000	1	8	100					9	9					
HMA TY-C	552	TON	500	2	9	100					10	11					
Clean-Up	1	EA	2	1	10	100					12	12					
<b>LOC.4 - (ROAD TO PIER)</b>	<b>7</b>	<b>DAYS</b>	<b>1</b>	<b>7</b>							12	18					
Setting Barricades	1	EA	2	1	11	100					13	13					
Place Traffic Control	1	EA	2	1	14	100					14	14					
Remove Material	997	SY	5000	1	15	100					15	15					
Flex Base Repair	997	SY	1500	1	16	100					16	16					
Prime Coat	199	GAL	4000	1	17	100					17	17					
HMA TY-C	115	TON	500	1	18	100					18	18					
Clean-Up	1	EA	2	1	19	100					19	19					
<b>LOC.6 - (FISHING PIER PARKING)</b>	<b>7</b>	<b>DAYS</b>	<b>1</b>	<b>7</b>							19	25					
Setting Barricades	1	EA	2	1	20	100					20	20					
Place Traffic Control	1	EA	2	1	23	100					21	21					
Remove Material	1,402	SY	5000	1	24	100					22	22					
Flex Base Repair	1,402	SY	1500	1	25	100					23	23					
Prime Coat	280	GAL	4000	1	26	100					24	24					
HMA TY-C	161	TON	500	1	27	100					25	25					
Clean-Up	1	EA	2	1	28	100					26	26					
<b>LOC.5 - (FISHING PIER)</b>	<b>9</b>	<b>DAYS</b>	<b>1</b>	<b>9</b>							26	34					
Setting Barricades	1	EA	2	1	29	100					27	27					
Place Traffic Control	1	EA	2	1	32	100					28	28					
Remove Material	1,664	SY	5000	1	33	100					29	29					
Flex Base Repair	1,664	SY	1500	2	34	100					30	31					
Prime Coat	333	GAL	4000	1	35	100					32	32					
HMA TY-C	191	TON	500	1	36	100					33	33					
Clean-Up	1	EA	2	1	37	100					34	34					

Remove Temporary Signs	1	EA	2	1	38	100				35	35
<b>LOC.1 - (BOAT RAMP)</b>	<b>13</b>	<b>DAYS</b>	<b>1</b>	<b>13</b>						35	47
Mobilization	1	EA	2	1	39	100				36	36
Setting Barricades	1	EA	2	1	42	100				37	37
Place Traffic Control	1	EA	2	1	43	100				38	38
Remove Material	3,665	SY	5000	1	44	100				39	39
Flex Base Repair	3,665	SY	1500	3	45	100				40	42
Prime Coat	733	GAL	8000	1	46	100				43	43
HMA TY-C	421	TON	500	1	47	100				44	44
Bonding Course	733	GAL	4000	1	48	100				45	45
HMA TY-B	527	TON	500	2	49	100				46	47
Clean-Up	1	EA	2	1	50	100				48	48
<b>LOC.2 - (BOAT RAMP PARKING)</b>	<b>9</b>	<b>DAYS</b>	<b>1</b>	<b>9</b>						48	56
Setting Barricades	1	EA	2	1	51	100				49	49
Place Traffic Control	1	EA	2	1	54	100				50	50
Remove Material	4,153	SY	5000	1	55	100				51	51
Flex Base Repair	4,153	SY	1500	3	56	100				52	54
Prime Coat	831	GAL	4000	1	57	100				55	55
HMA TY-C	478	TON	500	1	58	100				56	56
Clean-Up	1	EA	2	1	59	100				57	57
<b>LOC.7 - (CORRAL AREA)</b>	<b>7</b>	<b>DAYS</b>	<b>1</b>	<b>7</b>						57	63
Setting Barricades	1	EA	2	1	60	100				58	58
Place Traffic Control	1	EA	2	1	63	100				59	59
Remove Material	675	SY	5000	1	64	100				60	60
Flex Base Repair	675	SY	1500	1	65	100				61	61
Prime Coat	135	GAL	4000	1	66	100				62	62
HMA TY-C	78	TON	500	1	67	100				63	63
Clean-Up	1	EA	2	1	68	100				64	64
<b>LOC.8 - (CORRAL AREA PARKING)</b>	<b>8</b>	<b>DAYS</b>	<b>1</b>	<b>8</b>						64	71
Setting Barricades	1	EA	2	1	69	100				65	65
Place Traffic Control	1	EA	2	1	72	100				66	66
Remove Material	349	SY	5000	1	73	100				67	67
Flex Base Repair	349	SY	1500	1	74	100				68	68
Prime Coat	70	GAL	4000	1	75	100				69	69
HMA TY-C	40	TON	500	1	76	100				70	70
Clean-Up	1	EA	2	1	77	100				71	71
Remove Temporary Signs	1	EA	2	1	78	100				72	72
<b>ACCESIBLE CONC. RAMPS</b>	<b>17</b>	<b>DAYS</b>	<b>1</b>	<b>17</b>						72	88
Mobilization	1	EA	2	1	79	100				73	73
Setting Barricades	1	EA	2	1	82	100				74	74
Remove ADA Ramps	8	EA	2	4	83	100				75	78

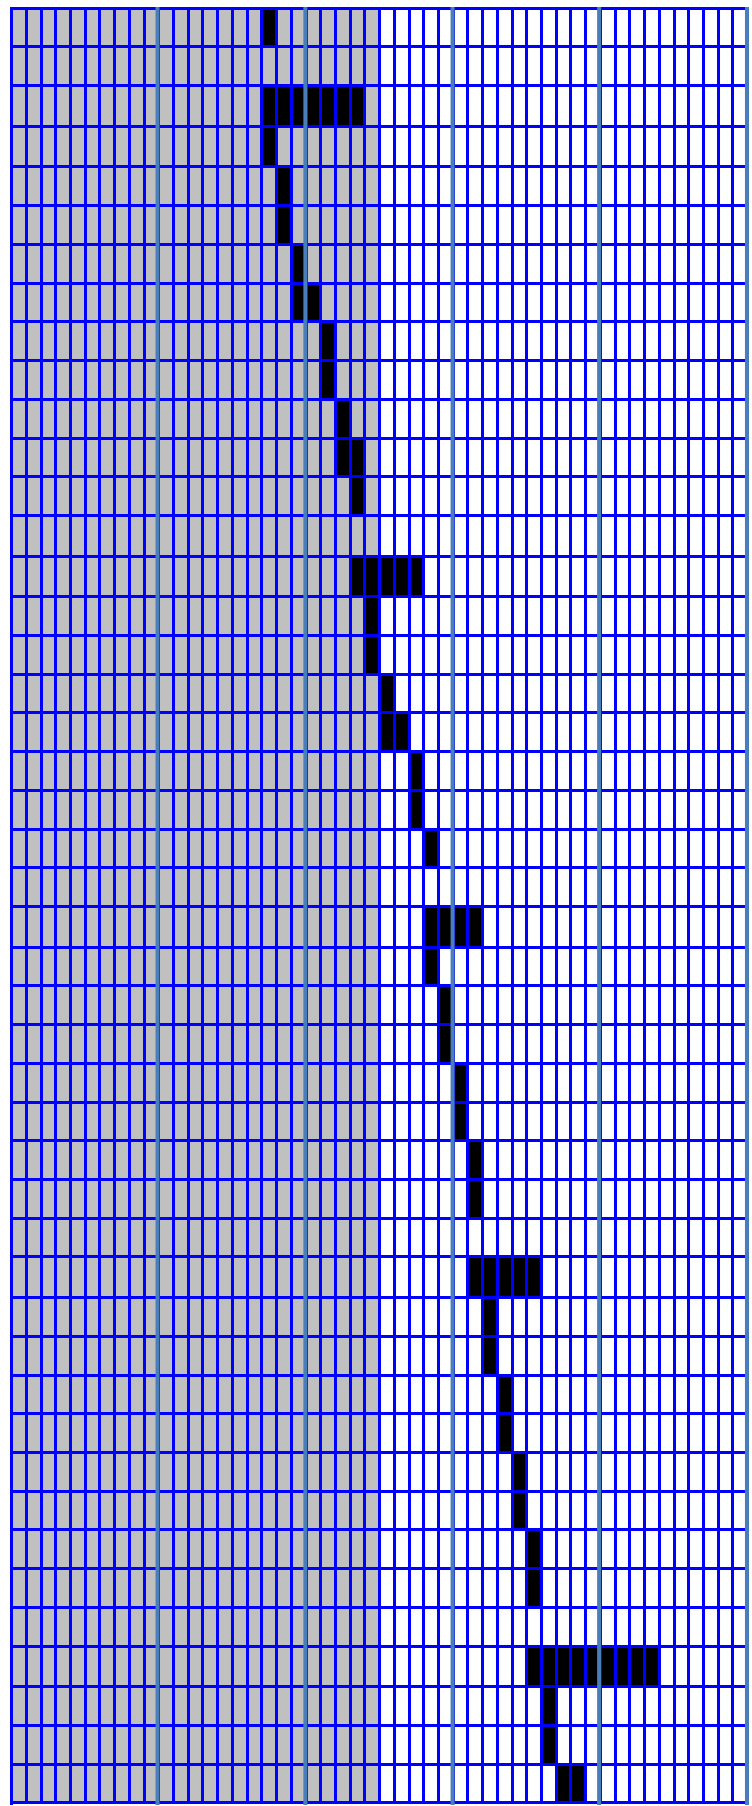

Install ADA Ramps	6	EA	1	6	84	100				79	84
Place Final Pavement Markings	5,098	LF	25000	1	85	100				85	85
Place Concrete Curb Stops	66	EA	40	2	86	100				86	87
Final Clean-Up	1	EA	2	1	87	100				88	88
Remove Final Barricade Signs	1	EA	2	1	88	100				89	89
<b>Estimated Begin Date:</b>											
9/1/2022											
<b>Estimated Completion Date:</b>											
1/13/2023											

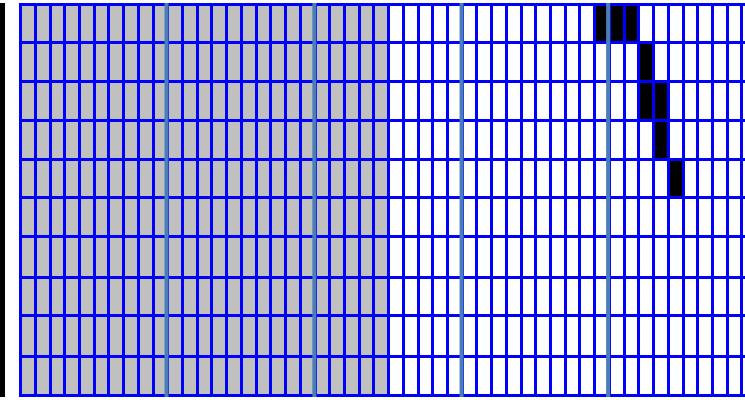

DocuSigned by:  
*Eliud*  
3F87CF7168DC4E4...

5/2/2022
