


Act ID	Description	Quantity	Unit	DPR	Original Duration	Early Start	Early Finish	Calendar	2022												2023												2024											
									JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC						
1000	CSJ:0336-03-072				1d	18JUL22	18JUL22	3	CSJ:0336-03-072																																			
1010	Place Barricades	1	LS	.2	5d	18JUL22	25JUL22	3	■ Place Barricades																																			
1020	Place SWP3 Items	1	LS	.25	4d	26JUL22	01AUG22	3	■ Place SWP3 Items																																			
1030	Remove Drainage Structure	105	EA	10	11d	02AUG22	18AUG22	3	■ Remove Drainage Structure																																			
1050	Driveway Pipes	294	EA	6	49d	22AUG22	09JAN23	3	■ Driveway Pipes																																			
1055	Roadway Culvert Extension	10	EA	.25	4d	10JAN23	16JAN23	3	■ Roadway Culvert Extension																																			
1065	Temporary Spl Shoring	420	SY	100	5d	17JAN23	21FEB23	3	■ Temporary Spl Shoring																																			
1070	Drainage Structure Wingwalls	9	EA	.2	45d	22FEB23	14JUN23	3	■ Drainage Structure Wingwalls																																			
1080	Remove / Install Metal Beam Guard Fence	18	EA	.75	24d	15JUN23	27JUL23	3	■ Remove / Install Metal Beam Guard Fence																																			
1120	Object Markers and Delineators	88	EA	100	1d	31JUL23	31JUL23	3	■ Object Markers and Delineators																																			
1130	Final Clean-Up	1	LS	.25	4d	01AUG23	07AUG23	3	■ Final Clean-Up																																			
1140	CSJ: 1678-02-007				1d	08AUG23	08AUG23	1	I CSJ: 1678-02-007																																			
1150	Place Barricades	1	LS	.2	5d	09AUG23	15AUG23	1	■ Place Barricades																																			
1160	Place SWP3 Items	1	LS	.25	4d	16AUG23	21AUG23	1	■ Place SWP3 Items																																			
1170	Prep ROW	141	STA	10	14d	22AUG23	12SEP23	1	■ Prep ROW																																			
1180	Remove Drainage Structures	20	EA	10	2d	13SEP23	14SEP23	1	I Remove Drainage Structures																																			
1200	Driveway Pipes	54	EA	6	9d	18SEP23	02OCT23	1	■ Driveway Pipes																																			
1210	Roadway Culvert Extension	7	HR	8	1d	03OCT23	03OCT23	1	■ Roadway Culvert Extension																																			
1215	Temporary Spl Shoring	570	SY	100	6d	05OCT23	16OCT23	1	■ Temporary Spl Shoring																																			
1220	Drainage Structure Box	55	LF	4	14d	17OCT23	05DEC23	1	■ Drainage Structure Box																																			
1230	Drainage Structure Wingwalls	12	EA	.2	60d	06DEC23	12JUN24	1	■ Drainage Structure Wingwalls																																			
1240	Remove / Install Metal Beam Guard Fence	1	EA	.75	2d	13JUN24	17JUN24	1	■ Remove / Install Metal Beam Guard Fence																																			
1270	Object Markers and Delineators	18	EA	100	1d	18JUN24	18JUN24	1	I Object Markers and Delineators																																			
1280	Final Clean-up	1	LS	.25	4d	19JUN24	25JUN24	1	■ Final Clean-up																																			
1290	CSJ: 2891-01-018				1d	26JUN24	26JUN24	1	CSJ: 2891-01-018																																			
1300	Place Barricades	1	LS	.2	5d	27JUN24	08JUL24	1	■ Place Barricades																																			
1310	Place SWP3 Items	1	LS	.25	4d	09JUL24	15JUL24	1	■ Place SWP3 Items																																			
1320	Prep ROW	351	STA	10	35d	16JUL24	10SEP24	1	■ Prep ROW																																			
1330	Remove Drainage Structure	62	EA	10	7d	11SEP24	23SEP24	1	■ Remove Drainage Structure																																			
1340	Driveway Pipes	177	EA	6	30d	24SEP24	12DEC24	1	■ Driveway Pipes																																			
1350	Roadway Culvert Extension	3	EA	.25	12d	13JAN25	12FEB25	1	■ Roadway Culvert Extension																																			
1360	Temporary Spl Shoring	3002	SF	100	30d	18FEB25	19MAY25	1	■ Temporary Spl Shoring																																			
1370	Drainage Structure Box	75	LF	4	19d	20MAY25	24JUN25	1	■ Drainage Structure Box																																			
1380	Drainage Structure Wingwalls	12	EA	.2	60d	25JUN25	20OCT25	1	■ Drainage Structure Wingwalls																																			
1390	Object Markers and Delineators	82	EA	100	1d	21OCT25	21OCT25	1	■ Object Markers and Delineators																																			
1400	Final Clean-Up	1	LS	.25	4d	22OCT25	28OCT25	1	■ Final Clean-Up																																			
1410	CSJ: 3220-01-13				1d	29OCT25	29OCT25	1	CSJ: 3220-01-13																																			
1420	Place Barricades	1	LS	.2	5d	30OCT25	12NOV25	1	■ Place Barricades																																			
1430	Place SWP3 Items	1	LS	.25	4d	13NOV25	19NOV25	1	■ Place SWP3 Items																																			
1440	Prep ROW	353	STA	10	36d	20NOV25	15APR26	1	■ Prep ROW																																			
1450	Remove Drainage Structure	9	EA	10	1d	16APR26	16APR26	1	■ Remove Drainage Structure																																			
1460	Driveway Pipes	61	EA	6	11d	20APR26	18MAY26	1	■ Driveway Pipes																																			
1470	Roadway Culvert Extension	13	EA	.25	52d	19MAY26	18AUG26	1	■ Roadway Culvert Extension																																			
1480	Temporary Spl Shoring	222	SF	100	3d	19AUG26	21AUG26	1	■ Temporary Spl Shoring																																			
1490	Drainage Structure Wingwalls	15	EA	.2	75d	24AUG26	13APR27	1	■ Drainage Structure Wingwalls																																			
1500	Remove / Install Metal Beam Guard Fence	4	EA	.75	6d	14APR27	22APR27	1	■ Remove / Install Metal Beam Guard Fence																																			
1510	Object Markers and Delineators	48	EA	100	1d	03MAY27	03MAY27	1	■ Object Markers and Delineators																																			
1520	Final Clean-Up	1	LS	.25	4d	04MAY27	10MAY27	1	■ Final Clean-Up																																			
TIME	TOTAL WORKING DAYS	683*			1d	11MAY27	11MAY27	1																																				

Start date	18JUL22
Finish date	11MAY27
Data date	18JUL22
Run date	01APR22
Page number	1A
© Primavera Systems, Inc.	

TXDOT
SH 103, ETC.
CSJ:0336-03-072, ETC.
683 WORKING DAYS
(Total Barricade Time: 59 Months)

DocuSigned by:
Elizabeth Ortega, P.E.
Elizabeth Ortega, P.E. #91106
4/1/2022

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

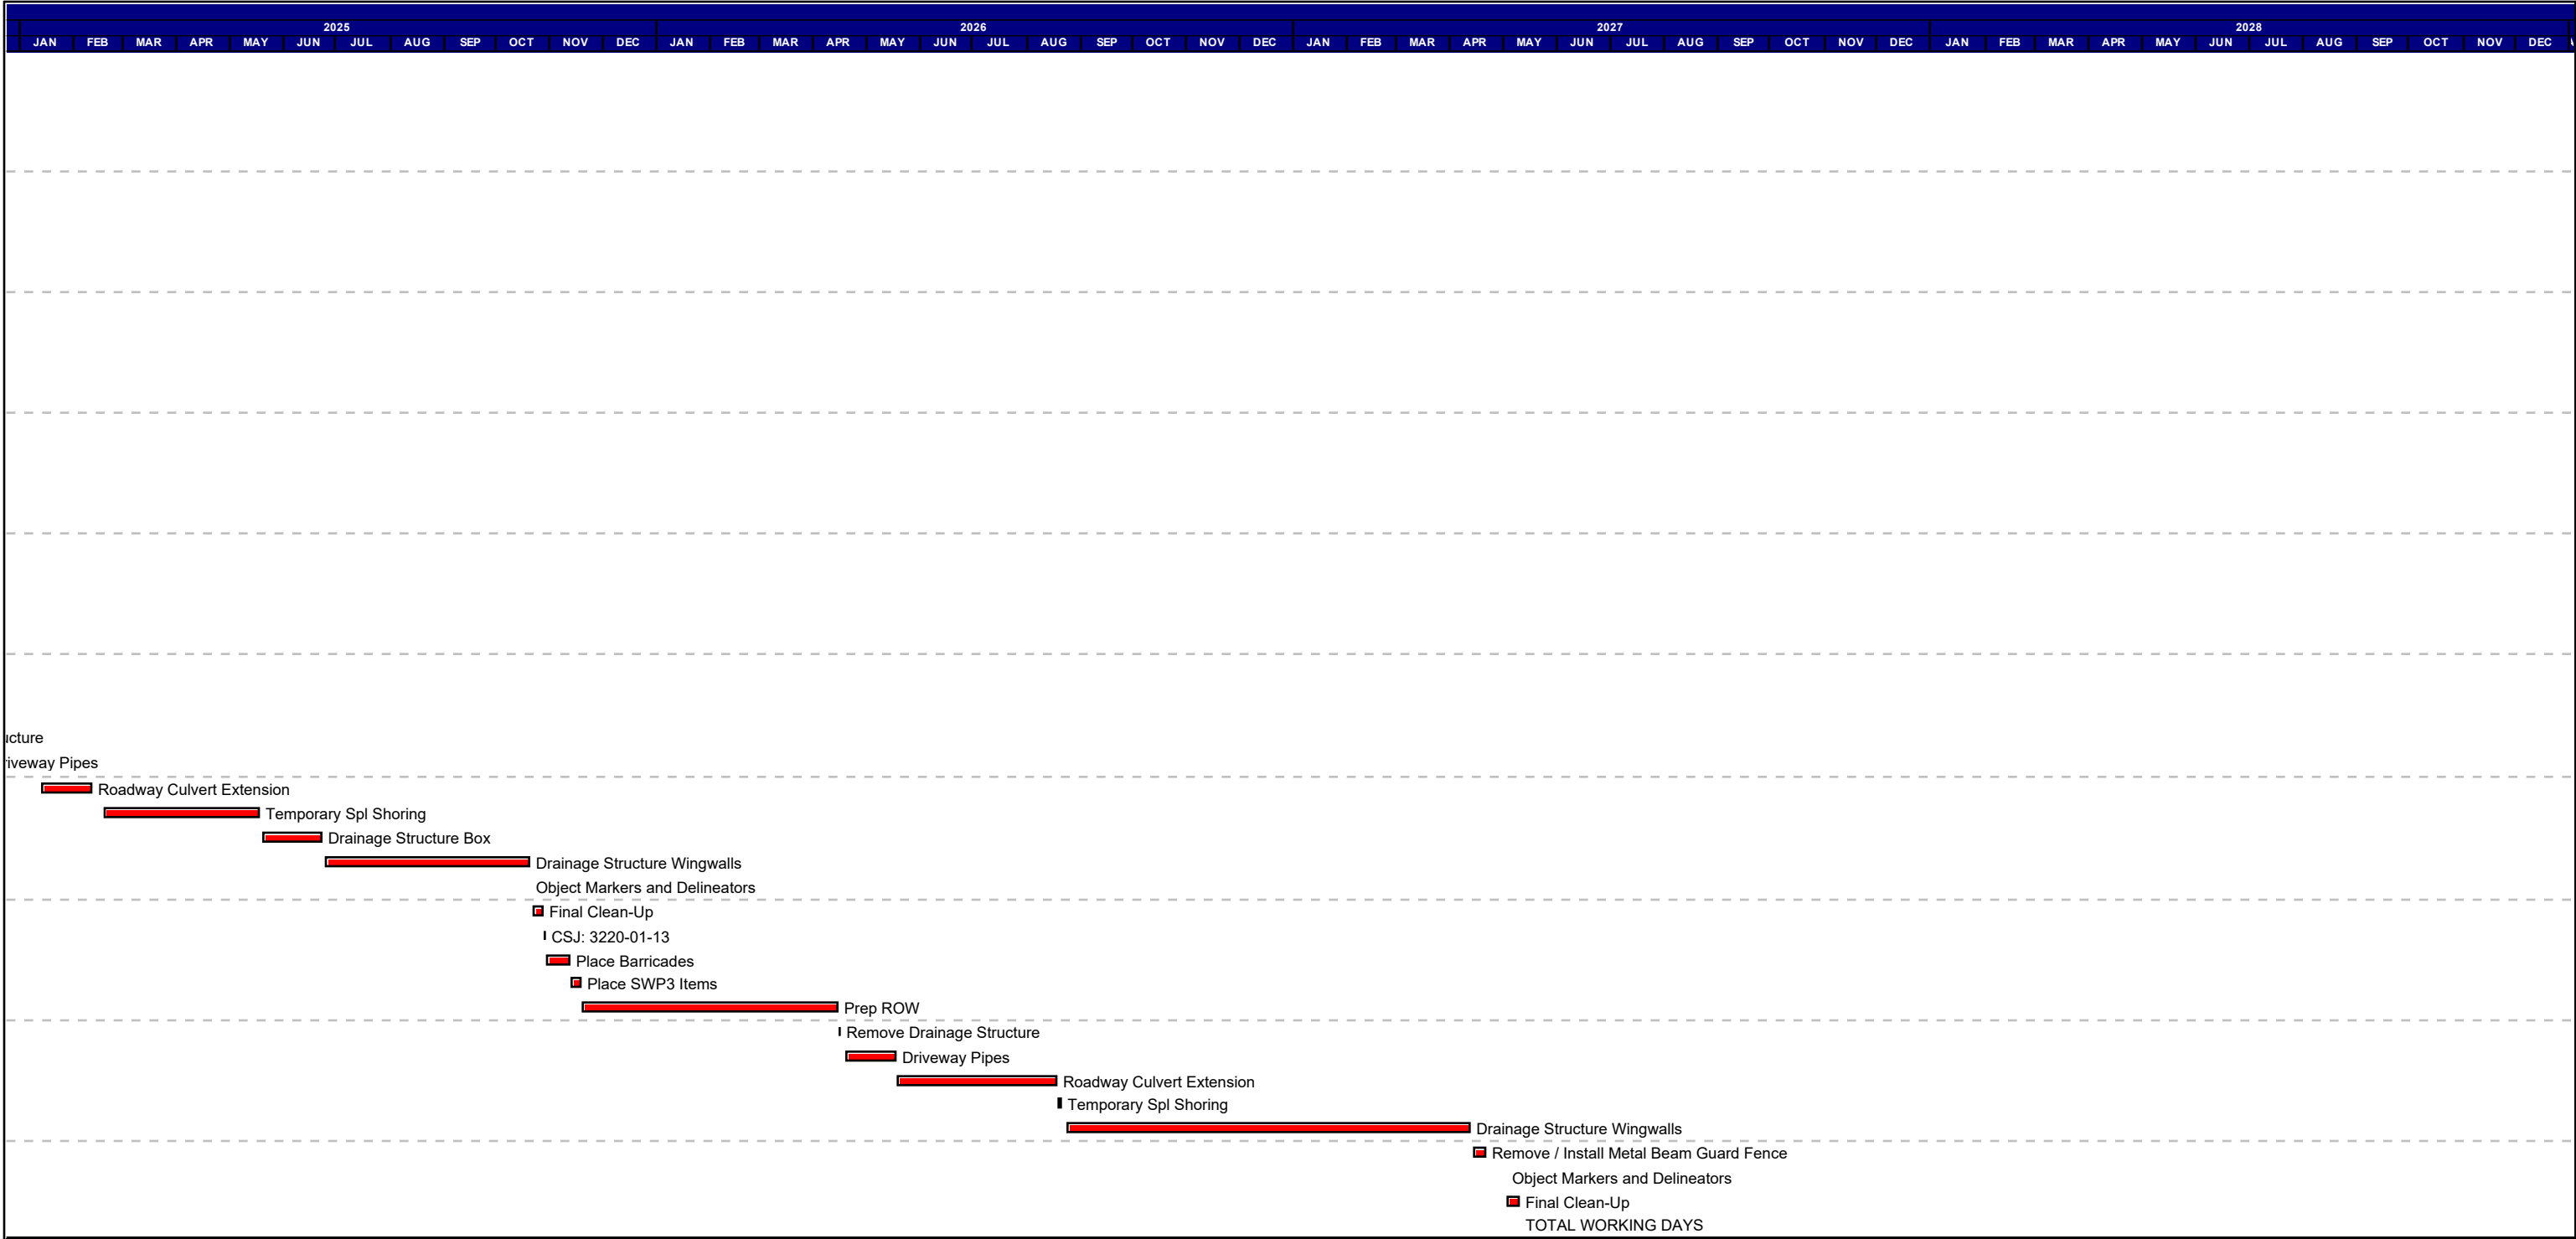

Start date	18JUL22
Finish date	11MAY27
Data date	18JUL22
Run date	01APR22
Page number	1B
© Primavera Systems, Inc.	

TXDOT
 SH 103, ETC.
 CSJ:0336-03-072, ETC.
 683 WORKING DAYS
 (Total Barricade Time: 59 Months)

DocuSigned by:
Elizabeth Ortega, P.E.
 Elizabeth Ortega, P.E. #91106
 4/1/2022

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point
