


ID	Task Name	Quantity	Units	Daily Production Rate	Duration	Start	Finish
1	FM2493 Project	0			918 days	Sat 4/1/23	Fri 12/24/27
2	Contract Award	0			0 days	Sat 4/1/23	Sat 4/1/23
3	Notice to Proceed	0			0 days	Mon 7/24/23	Mon 7/24/23
4	Construction Timeline	0			858 days	Mon 7/24/23	Fri 12/24/27
5	Phase 1 Utility Delay after Letting	0			1 day	Mon 7/24/23	Wed 7/26/23
6	Phase 1	0			397 days	Thu 8/3/23	Wed 8/20/25
7	Phase 1A FM 2494 STA 582+00 to STA 728+75 (RT)	0			214 days	Thu 8/3/23	Wed 9/11/24
8	Place Advance Warning Signs	2	D	1	2 days	Thu 8/3/23	Wed 8/9/23
9	Place SW3P Measures	2	D	1	2 days	Thu 8/3/23	Wed 8/9/23
10	Prep ROW	30	Acre	3	10 days	Wed 8/9/23	Fri 8/25/23
11	Excavation	54556	CY	2000	27 days	Thu 8/17/23	Fri 10/6/23
12	Embankment	22332	CY	2000	11 days	Fri 10/6/23	Fri 10/27/23
13	temp Special Shoring	650	SF	100	7 days	Fri 10/13/23	Fri 10/27/23
14	Place 3X2 RCB	602	LF	70	10 days	Thu 10/19/23	Mon 11/6/23
15	Place 8x6 RCB	264	LF	70	4 days	Mon 11/6/23	Wed 11/15/23
16	18" RCP	5533	LF	240	23 days	Wed 11/15/23	Wed 12/27/23
17	24" RCP	4000	LF	240	17 days	Wed 12/27/23	Mon 1/29/24
18	30" RCP	2670	LF	240	11 days	Mon 1/29/24	Fri 2/16/24
19	Inlets, manholes	49	EACH	2	25 days	Fri 1/19/24	Thu 3/7/24
20	Treated Base	73117	SY	2500	28 days	Fri 2/2/24	Wed 3/27/24
21	Flex Base	74716	CY	750	100 days	Mon 2/12/24	Mon 8/19/24
22	Place HMA	15168	Ton	1000	15 days	Thu 8/8/24	Thu 9/5/24
23	Temp Pave (Detours)	1856	Ton	1000	2 days	Thu 9/5/24	Wed 9/11/24
24	Phase 1B FM 2494 STA 582+00 to STA 728+75 (LT)	0			183 days	Wed 9/11/24	Wed 8/20/25
25	Place Advance Warning Signs	2	D	1	2 days	Wed 9/11/24	Fri 9/13/24
26	Place SW3P Measures	2	D	1	2 days	Wed 9/11/24	Fri 9/13/24
27	Prep ROW	30	Acre	3	10 days	Fri 9/13/24	Thu 10/3/24
28	Pavement Removal	52756	SY	2000	27 days	Mon 9/23/24	Wed 11/13/24
29	Excavation	54556	CY	2000	27 days	Thu 10/3/24	Fri 11/22/24
30	Embankment	22332	CY	2000	11 days	Fri 11/22/24	Thu 12/12/24
31	Place 3X2 RCB	602	LF	70	9 days	Thu 12/5/24	Mon 12/23/24
32	Place 8x6 RCB	264	LF	70	4 days	Mon 12/23/24	Mon 12/30/24
33	18" RCP	1822	LF	120	15 days	Mon 12/30/24	Mon 1/27/25
34	Inlets, manholes	49	EACH	2	25 days	Mon 1/13/25	Fri 2/14/25
35	Treated Base	73117	SY	2500	28 days	Mon 1/13/25	Thu 3/6/25
36	Flex Base	74716	CY	750	100 days	Wed 1/22/25	Wed 7/30/25
37	Place HMA	15168	Ton	1000	15 days	Fri 7/18/25	Fri 8/15/25
38	Temp Pave (Detours)	1856	Ton	1000	2 days	Fri 8/15/25	Wed 8/20/25
39	Phase 2	0			197 days	Thu 8/21/25	Wed 8/26/26
40	Phase 2A FM 2494 STA 782+00 to STA 788+66 (RT)	0			78 days	Thu 8/21/25	Wed 1/14/26
41	Place Advance Warning Signs	2	D	1	2 days	Thu 8/21/25	Mon 8/25/25
42	Place SW3P Measures	2	D	1	2 days	Thu 8/21/25	Mon 8/25/25
43	Prep ROW	12	Acre	3	4 days	Mon 8/25/25	Mon 9/1/25
44	Excavation	22272	CY	2000	11 days	Wed 9/3/25	Wed 9/24/25
45	Embankment	9117	CY	2000	5 days	Wed 9/24/25	Thu 10/2/25
46	temp Special Shoring	277	SF	100	3 days	Thu 9/18/25	Wed 9/24/25




*Randee Morris*  
04/04/2023

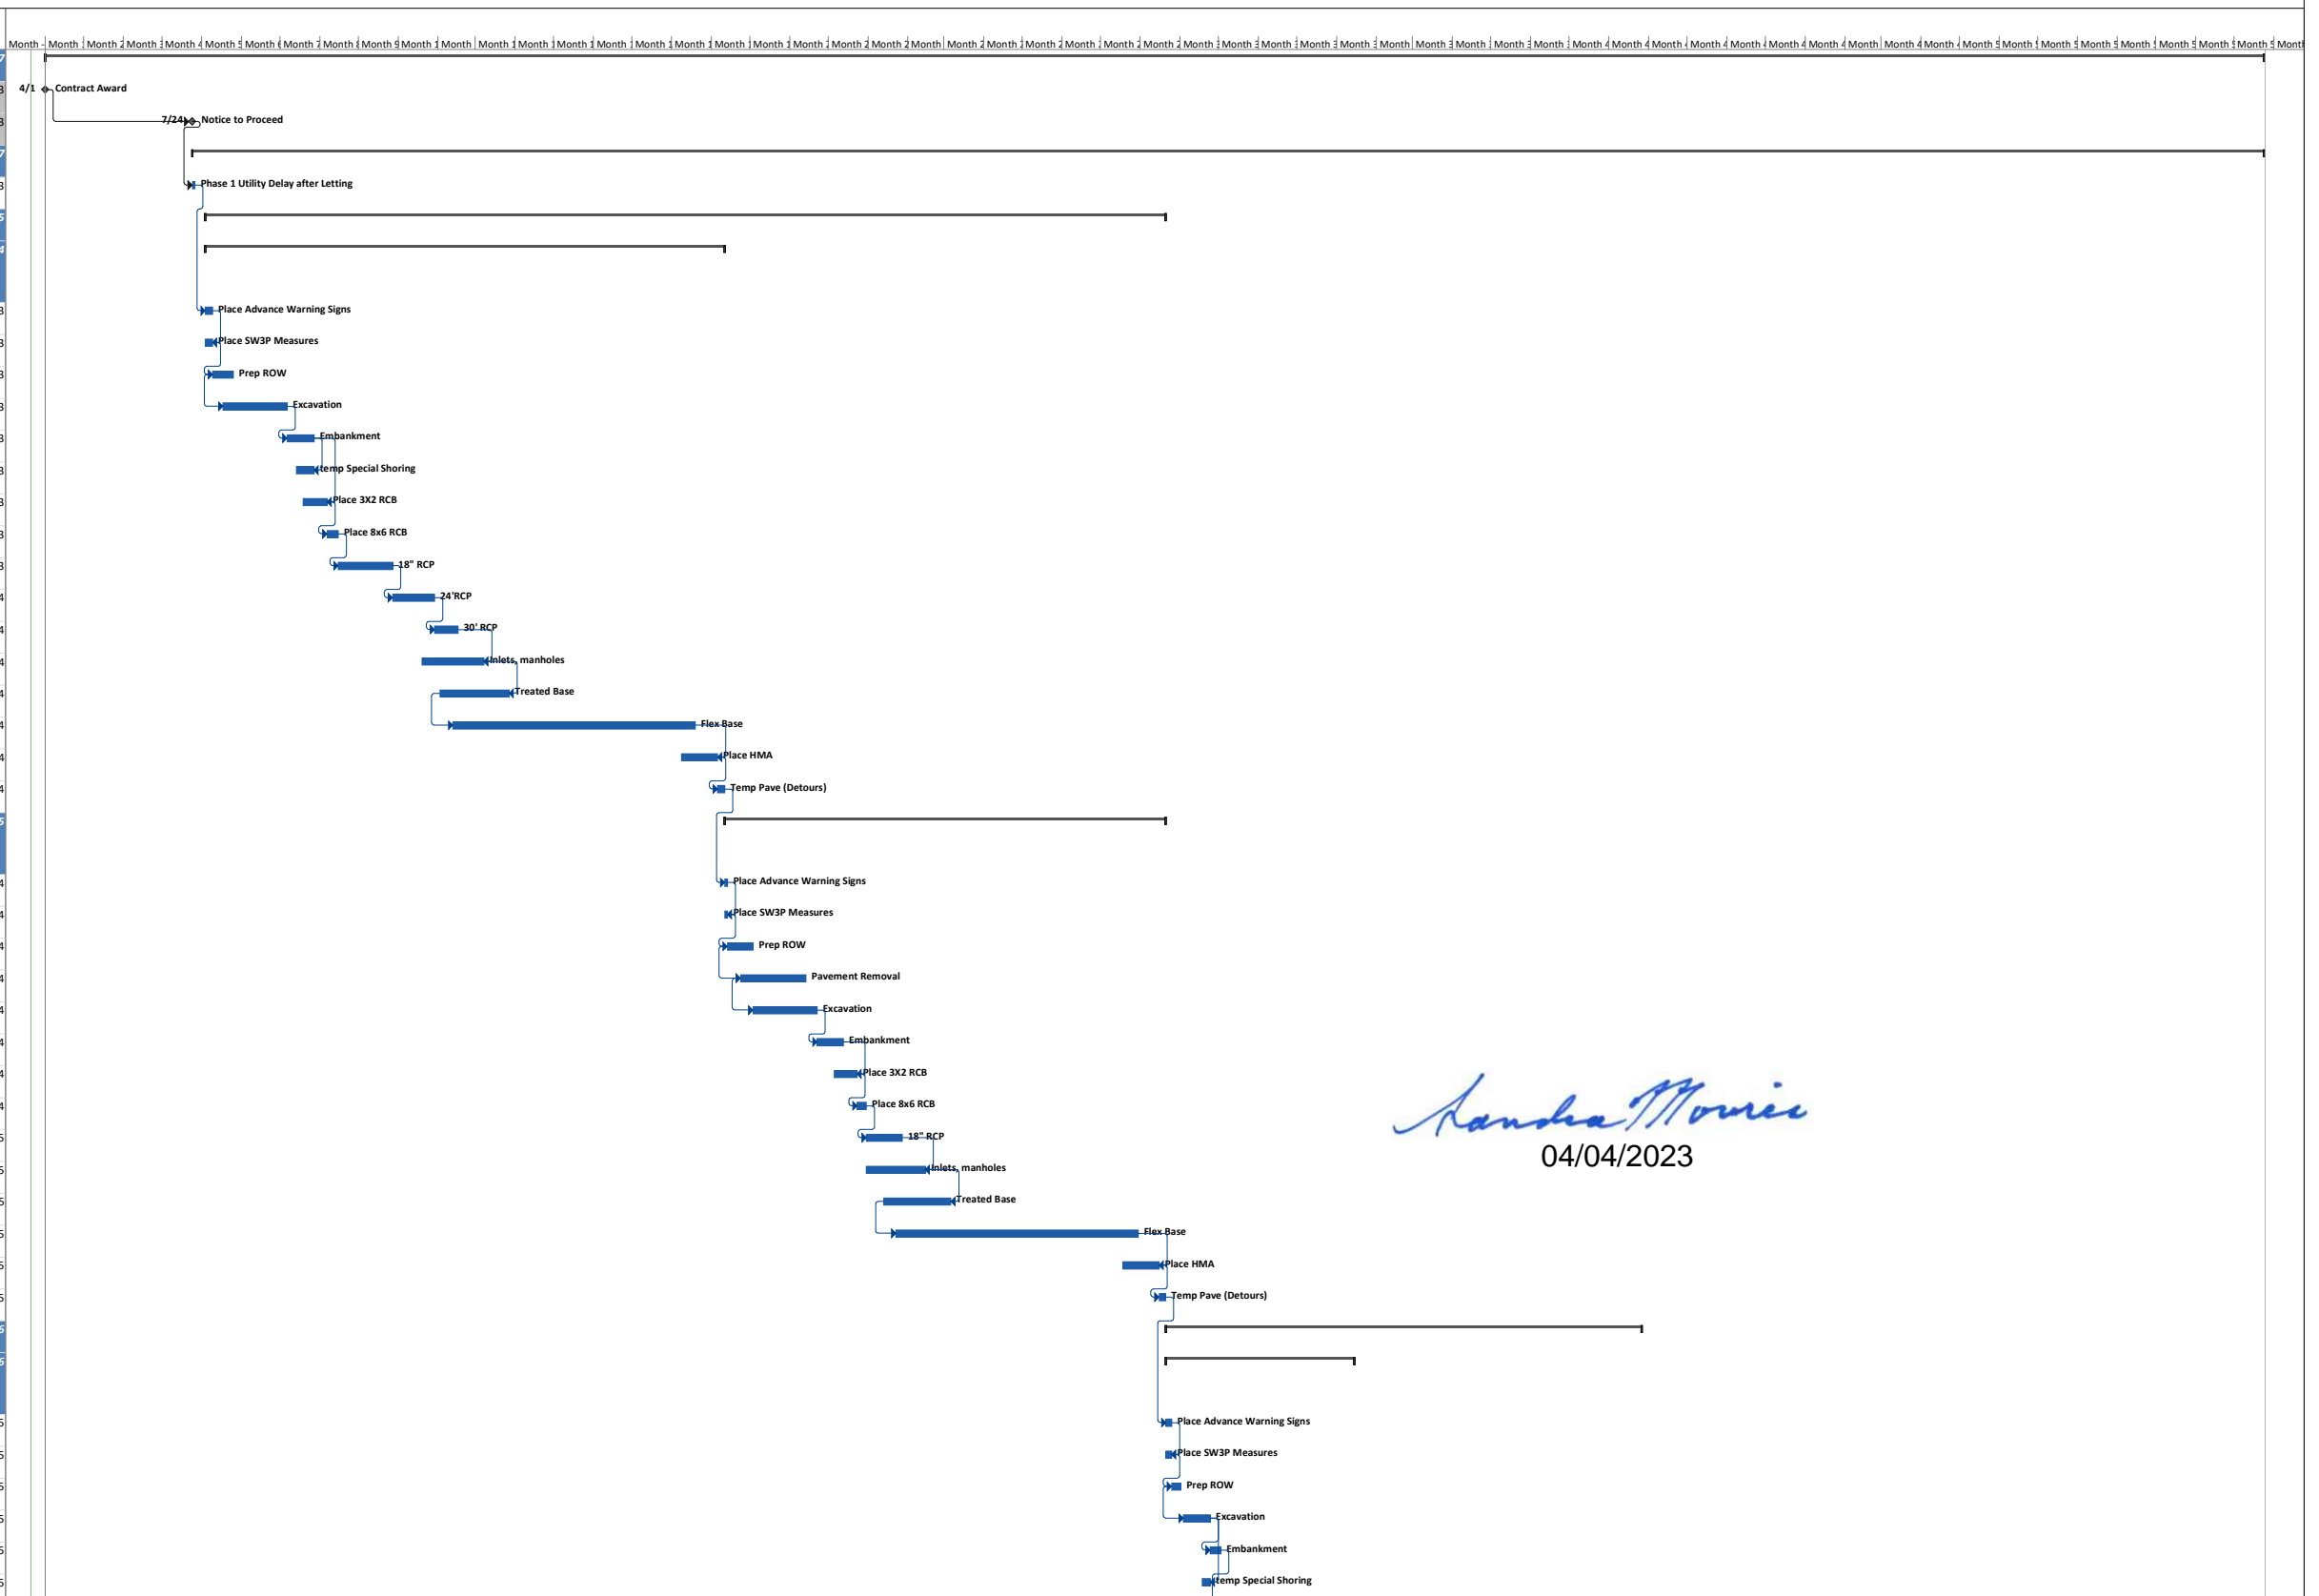

Task	Milestone	Project Summary	External Milestone	Inactive Milestone	Manual Task	Manual Summary Rollup	Start-only	Deadline	Manual Progress
Split	Summary	External Tasks	Inactive Task	Inactive Summary	Duration-only	Manual Summary	Finish-only	Progress	


ID	Task Name	Quantity	Units	Daily Production Rate	Duration	Start	Finish
47	Place 3X2 RCB	192	LF	70	3 days	Thu 10/2/25	Wed 10/8/25
48	Place 8x6 RCB	339	LF	70	5 days	Wed 10/8/25	Fri 10/17/25
49	18" RCP	1500	LF	120	12 days	Fri 10/17/25	Mon 11/10/25
50	Place 24" RCP	496	LF	120	4 days	Mon 11/10/25	Mon 11/17/25
51	Place 30" RCP	488	LF	120	4 days	Mon 11/17/25	Mon 11/24/25
52	Place 36" RCP	224	LF	120	2 days	Mon 11/24/25	Thu 11/27/25
53	Inlets, manholes	45	EACH	2	23 days	Wed 11/5/25	Wed 12/17/25
54	Treated Base	29850	SY	2500	12 days	Wed 10/15/25	Thu 11/6/25
55	Flex Base	30502	CY	750	41 days	Thu 10/23/25	Thu 1/8/26
56	Place HMA	6192	Ton	1000	6 days	Thu 1/1/26	Mon 1/12/26
57	Temp Pave (Detours)	758	Ton	1000	1 day	Mon 1/12/26	Wed 1/14/26
58	Phase 2B FM 2494 STA 582+00 to STA 782+00 (LT)	0			119 days	Wed 1/14/26	Wed 8/26/26
59	Place Advance Warning Signs	2	D	1	2 days	Wed 1/14/26	Mon 1/19/26
60	Place SW3P Measures	2	D	1	2 days	Wed 1/14/26	Mon 1/19/26
61	Prep ROW	12	Acre	3	4 days	Mon 1/19/26	Mon 1/26/26
62	Pavement Removal	21537	SY	3000	7 days	Mon 1/26/26	Fri 2/6/26
63	Excavation	22272	CY	2000	11 days	Wed 2/4/26	Wed 2/25/26
64	Embankment	9117	CY	2000	5 days	Wed 2/25/26	Thu 3/5/26
65	Place 3X2 RCB	192	LF	70	3 days	Thu 3/5/26	Thu 3/12/26
66	Place 8x6 RCB	339	LF	70	5 days	Thu 3/12/26	Fri 3/20/26
67	18" RCP	1682	LF	120	14 days	Fri 3/20/26	Thu 4/16/26
68	Place 24" RCP	496	LF	120	4 days	Thu 4/16/26	Thu 4/23/26
69	Place 30" RCP	488	LF	120	4 days	Thu 4/23/26	Fri 5/1/26
70	Place 36" RCP	224	LF	120	2 days	Fri 5/1/26	Wed 5/6/26
71	Inlets, manholes	49	EACH	1	49 days	Thu 2/12/26	Thu 5/14/26
72	Treated Base	29849	SY	2500	12 days	Mon 5/11/26	Wed 6/3/26
73	Flex Base	30502	CY	750	41 days	Wed 5/20/26	Thu 8/6/26
74	Place HMA	6197	Ton	1000	6 days	Thu 8/13/26	Mon 8/24/26
75	Temp Pave (Detours)	758	Ton	1000	1 day	Mon 8/24/26	Wed 8/26/26
76	Phase 3	0			234 days	Wed 8/26/26	Wed 11/10/27
77	Phase 3A FM 2494 STA 510+73 to STA 582+00 (RT)	0			129 days	Wed 8/26/26	Mon 4/26/27
78	Place Advance Warning Signs	2	D	1	2 days	Wed 8/26/26	Mon 8/31/26
79	Place SW3P Measures	2	D	1	2 days	Wed 8/26/26	Mon 8/31/26
80	Prep ROW	15	Acre	3	5 days	Mon 8/31/26	Wed 9/9/26
81	Excavation	26564	CY	2000	13 days	Wed 9/9/26	Fri 10/2/26
82	Embankment	10789	CY	2000	5 days	Fri 10/2/26	Mon 10/12/26
83	temp Special Shoring	277	SF	100	3 days	Wed 10/7/26	Mon 10/12/26
84	Place 8 x 5 RCB	200	LF	70	3 days	Mon 10/12/26	Mon 10/19/26
85	Place 10 X 5 RCB	65	LF	70	1 day	Mon 10/19/26	Wed 10/21/26
86	18" RCP	3182	LF	120	27 days	Wed 10/21/26	Thu 12/10/26
87	24" RCP	1004	LF	120	8 days	Thu 12/10/26	Thu 12/24/26
88	30" RCP	2581	LF	120	22 days	Thu 12/24/26	Thu 2/4/27
89	Inlets, manholes	25	EACH	1	25 days	Thu 2/4/27	Wed 3/24/27
90	Treated Base	35327	SY	2500	14 days	Fri 3/5/27	Thu 4/1/27
91	Flex Base	34700	CY	750	47 days	Wed 1/13/27	Mon 4/12/27
92	Place HMA	8450	Ton	1000	8 days	Mon 4/5/27	Wed 4/21/27
93	Concrete Pavement	1210	SY	540	3 days	Wed 4/21/27	Mon 4/26/27

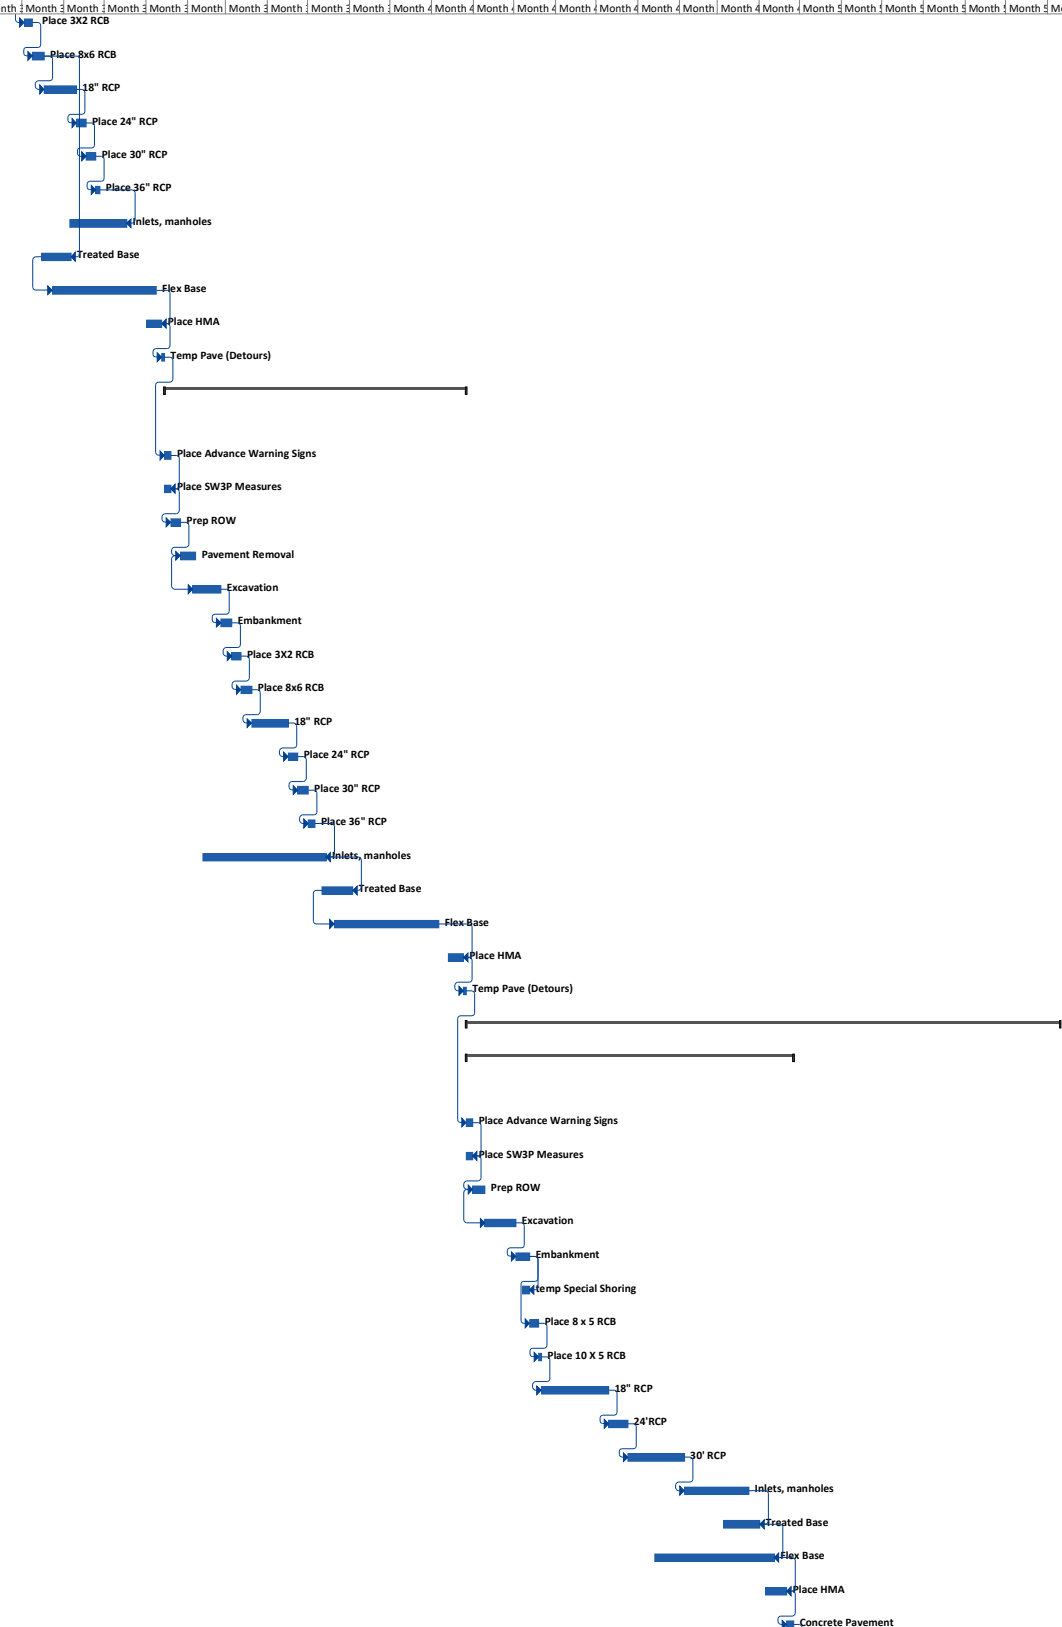

Task Split: █ Milestone ◆ Project Summary █ External Milestone ◆ Inactive Milestone █ Manual Task █ Manual Summary Rollup █ Start-only █ Deadline █ Manual Progress

Summary: ●●●●● Summary █ Inactive Task ◆ Inactive Summary █ Duration-only █ Manual Summary █ Finish-only █ Progress

ID	Task Name	Quantity	Units	Daily Production Rate	Duration	Start	Finish
94	Phase 3B FM 2494 STA 510+73 to STA 582+00	0			105 days	Mon 4/26/27	Wed 11/10/27
95	Place Advance Warning Signs	2	D	1	2 days	Mon 4/26/27	Thu 4/29/27
96	Place SW3P Measures	2	D	1	2 days	Mon 4/26/27	Thu 4/29/27
97	Prep ROW	15	Acre	3	5 days	Thu 4/29/27	Mon 5/10/27
98	Pavement Removal	26530	SY	2500	11 days	Mon 5/10/27	Mon 5/31/27
99	Excavation	22272	CY	2000	12 days	Wed 5/19/27	Thu 6/10/27
100	Embankment	9535	CY	2000	5 days	Thu 6/10/27	Fri 6/18/27
101	Place 8 x 5 RCB	200	LF	70	3 days	Fri 6/18/27	Thu 6/24/27
102	Place 10 X 5 RCB	65	LF	70	1 day	Fri 6/25/27	Mon 6/28/27
103	Place 18" RCP	282	LF	120	2 days	Mon 6/28/27	Thu 7/1/27
104	Inlets, manholes	25	EACH	1	25 days	Thu 7/1/27	Wed 8/18/27
105	Treated Base	35327	SY	2500	14 days	Fri 7/30/27	Thu 8/26/27
106	Flex Base	30502	CY	750	42 days	Mon 8/9/27	Thu 10/28/27
107	Place HMA	8450	Ton	1000	8 days	Thu 10/21/27	Fri 11/5/27
108	Concrete Pavement	1210	SY	540	2 days	Fri 11/5/27	Wed 11/10/27
109	Phase 4 Final Lift and Stripe	0			24 days	Wed 11/10/27	Fri 12/24/27
110	Super Pave	27623	Tons	2000	14 days	Wed 11/10/27	Mon 12/6/27
111	Striping	163500	LF	15000	10 days	Mon 12/6/27	Fri 12/24/27

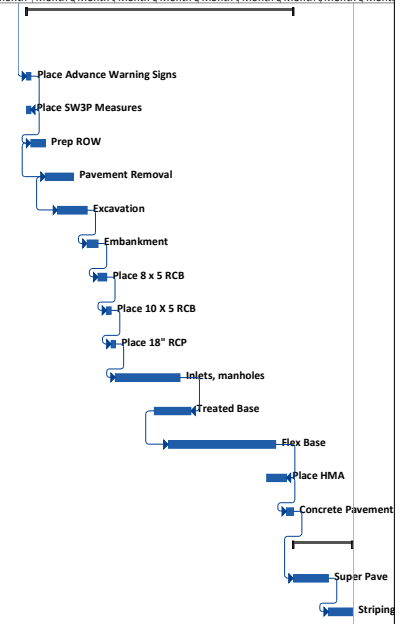

Task Split, Milestone, Project Summary, External Milestone, Inactive Milestone, Manual Task, Manual Summary Rollup, Start-only, Deadline, Manual Progress, Summary, External Tasks, Inactive Task, Inactive Summary, Duration-only, Manual Summary, Finish-only, Progress
