


Contract Time Estimate

Rd: VARIOUS County: GREGG, ETC
 CSJ: 0910-07-081 Project: STP 2B20(194)HES

TASK #	Description	Quantity	Unit	Daily Rate	Duration	Pred Task	% Comp	Pred Task	% Comp	Pred Task	% Comp	Start Day	Finish Day
1	Install Project Signing	1	LS	0.5	2							1	2
2	Begin Installing SW3P	1	LS	1	1	1	100					3	3
3	Remove Concrete	23	SY	20	2	2	100					4	5
4	Place Embankment	31	EA	2	16	3	100					6	21
5	Place Seeding	10,532	SY	1000	11	4	75					18	28
6	Install MBGF	50	EA	3	17	4	50					14	30
7	Install Riprap	2	CY	1	2	6	100					31	32
8	Final Clean-up	1	DAY	1	1	7	100					33	33
9													

1

= # Days / Cell

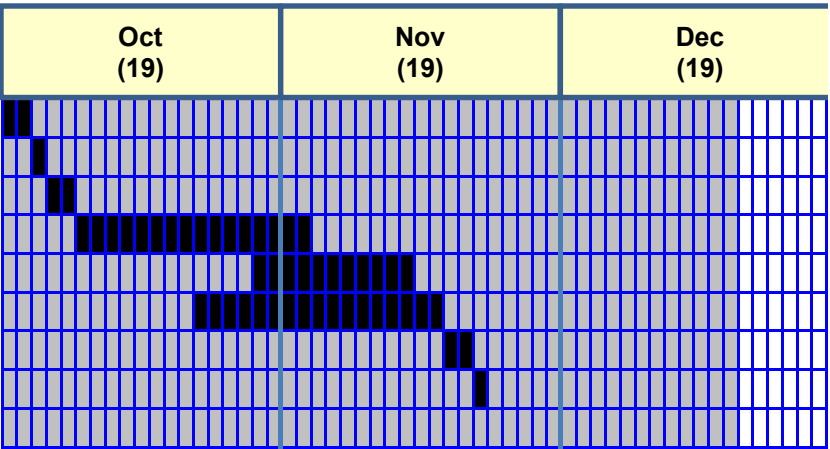

33 Contract Days
2 Months Barricades
