


ID	Task Name	Quantity	Unit	Production Rate (unit/day)	Duration	Start	Finish	Qtr 4, 2020			Qtr 1, 2021			Qtr 2, 2021			Qtr 3, 2021			Qtr 4, 2021			Qtr 1, 2022			Qtr 2, 2022			Qtr 3, 2022						
								Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug					
1	US 183 WA#6 - Total Project	0		0	569 days	Thu 10/1/20	Tue 12/6/22																												
2	Contract Award	0		0	1 day	Thu 10/1/20	Thu 10/1/20																												
3	Notice to Proceed	0		0	1 day	Mon 1/4/21	Mon 1/4/21																												
4	Construction Timeline	0		0	501 days	Tue 1/5/21	Tue 12/6/22																												
5	Phase 1 - Level Up & Widen NB Pavement	0		0	210 days	Tue 1/5/21	Mon 10/25/21																												
6	Set Perimeter Signs & Barricades	14.39	Miles	5	3 days	Tue 1/5/21	Thu 1/7/21																												
7	Set Erosion Control Devices	14.39	Miles	1.5	10 days	Fri 1/8/21	Thu 1/21/21																												
8	Prepare ROW	2.6	ACRES	1	5 days	Fri 1/22/21	Thu 1/28/21																												
9	Install RCP/CMP Pipes	8	LF	50	1 day	Fri 1/29/21	Fri 1/29/21																												
10	Install Headwall	1	EA	1	1 day	Mon 2/1/21	Mon 2/1/21																												
11	Extend Box Culverts	614	LF	15	45 days	Tue 2/2/21	Mon 4/5/21																												
12	Install Wingwalls/Headwalls	58	EA	1	58 days	Tue 4/6/21	Thu 6/24/21																												
13	Excavation/Embankment	46381	CY	1200	39 days	Tue 4/6/21	Fri 5/28/21																												
14	Cement Treated Subgrade	87350	SY	3500	25 days	Mon 6/7/21	Fri 7/9/21																												
15	Hot Mix (TY B) Base	27863	TON	800	35 days	Mon 7/26/21	Fri 9/10/21																												
16	Install T552 Retrofit Rail	36	LF	150	1 day	Mon 9/13/21	Mon 9/13/21																												
17	Topsoil/Seeding	216403	SY	7000	31 days	Mon 9/13/21	Mon 10/25/21																												
18	Phase 2 - Widen Southbound Pavement	0		0	196 days	Tue 10/26/21	Tue 7/26/22																												
19	TCP Striping/Eliminate Pvmnt Markings	304000	LF	10000	31 days	Tue 10/26/21	Tue 12/7/21																												
20	Set TCP Signs & Channelization Devices	14.39	Miles	5	4 days	Wed 12/8/21	Mon 12/13/21																												
21	Set Erosion Control Devices	14.39	Miles	1.5	10 days	Tue 12/14/21	Mon 12/27/21																												
22	Excavation/Embankment	46381	CY	1200	45 days	Tue 12/28/21	Mon 2/28/22																												
23	Cement Treated Subgrade	87350	SY	3500	25 days	Tue 3/8/22	Mon 4/11/22																												
24	Hot Mix (TY B) Base	27863	TON	800	35 days	Tue 4/26/22	Mon 6/13/22																												
25	Install T552 Retrofit Rail	36	LF	150	1 day	Tue 6/14/22	Tue 6/14/22																												
26	Topsoil/Seeding	216403	SY	7000	31 days	Tue 6/14/22	Tue 7/26/22																												
27	Phase 3 - Final Overlay and Striping	0		0	90 days	Wed 8/3/22	Tue 12/6/22																												
28	Set TCP Signs & Channelization Devices	14.39	Miles	5	4 days	Wed 8/3/22	Mon 8/8/22																												
29	Place Final Overlay (Superpave)	41569	TON	1500	28 days	Tue 8/16/22	Thu 9/22/22																												
30	TY I Striping & Pvmnt Markers	313036	LF	10000	32 days	Mon 9/5/22	Tue 10/18/22																												
31	Signs/object markers	116	EA	8	15 days	Wed 10/19/22	Tue 11/8/22																												
32	Punch List/Cleanup	14.39	Miles	1	20 days	Wed 11/9/22	Tue 12/6/22																												



Brian Enns, P.E.

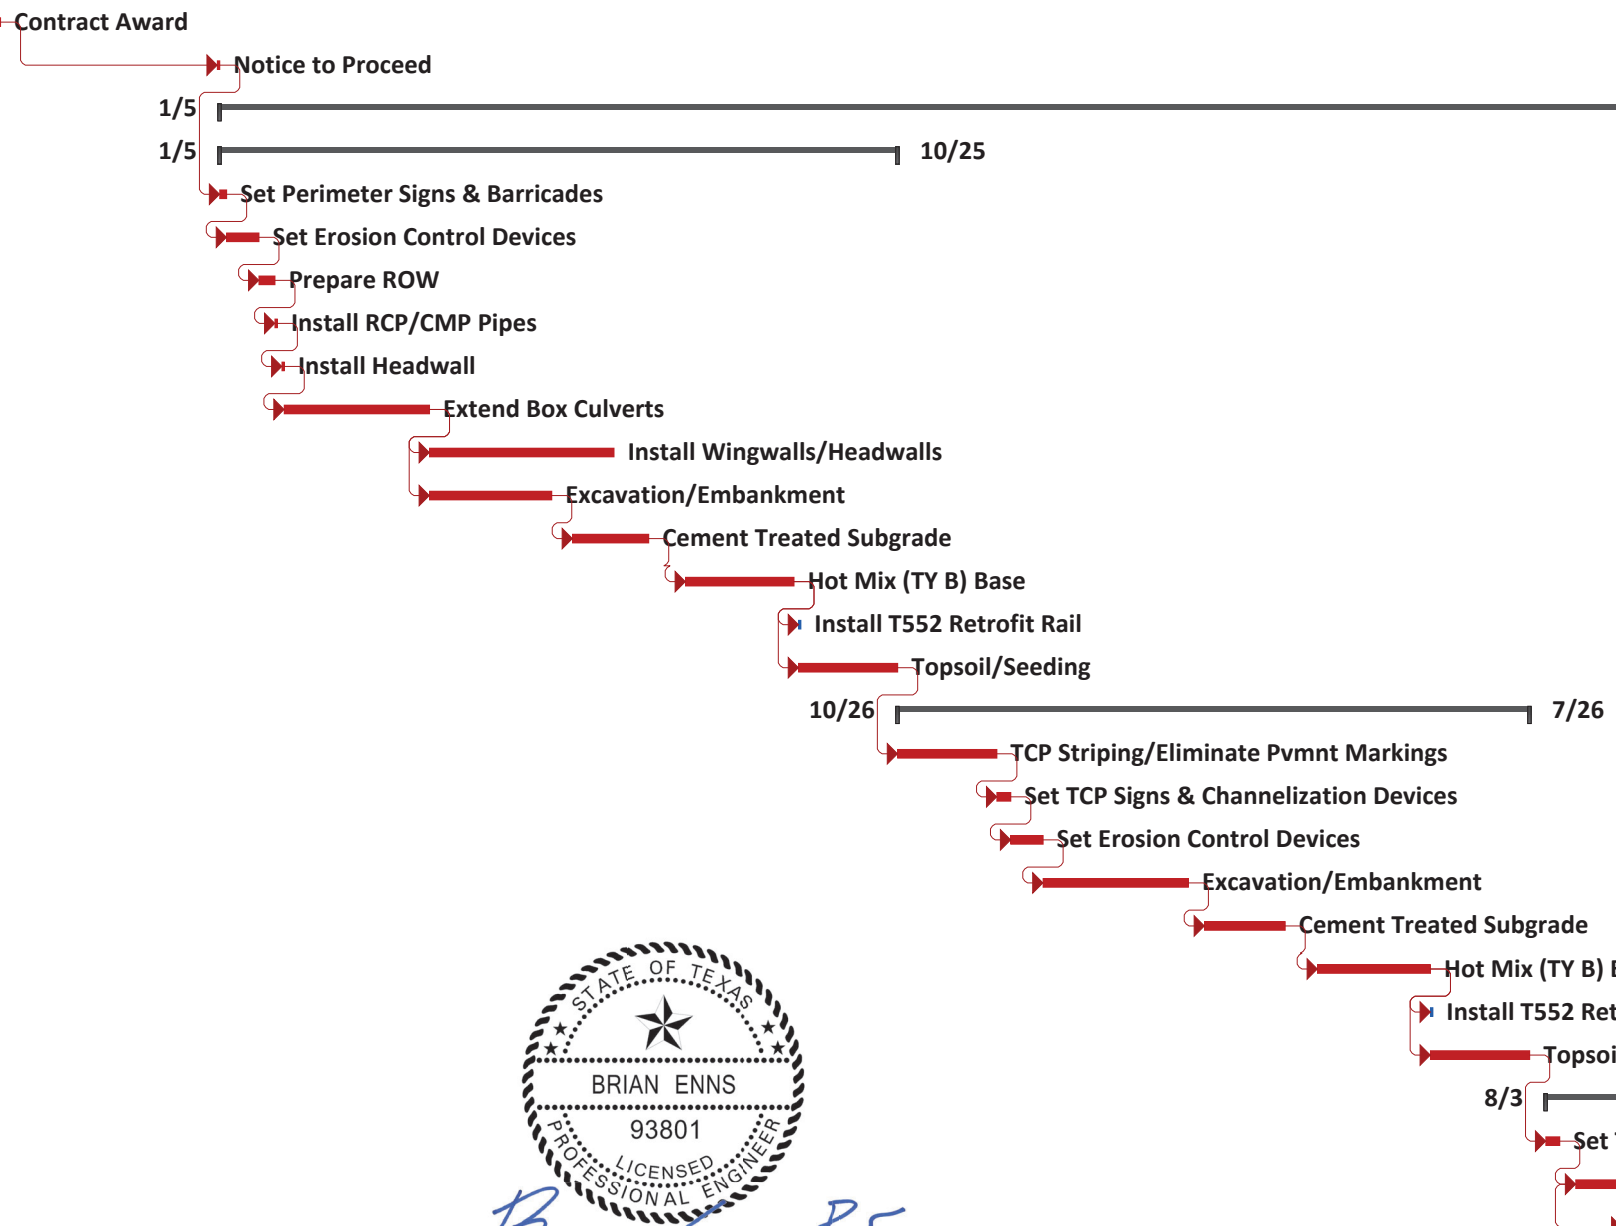

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Critical	
Milestone		External Milestone		Manual Task		Start-only		Critical Split	
Summary		Inactive Task		Duration-only		Finish-only		Progress	
