ID	Task Name	Quantity	Unit	Daily Rate	Duration	Start	Finish
1	Mobilization, Barricades & Temp Pavement	1	LS	0.5	2 days	Mon 3/2/20	Tue 3/3/20
2	Phase 1 SW3P	945	LF	500	2 days	Wed 3/4/20	Thu 3/5/20
3	Prep ROW	8	EA	5	2 days	Mon 3/9/20	Wed 3/11/20
4	Phase 1 Temp Shoring w/ DS	140	SF	30	5 days	Wed 3/11/20	Thu 3/19/20
5	Phase 1 Const Detours	373	SY	100	4 days	Thu 3/19/20	Mon 3/30/20
6	Phase 2 TCP	1	LS	1	1 day	Mon 3/30/20	Tue 3/31/20
7	Phase 2 SW3P	560	LF	500	1 day	Tue 3/31/20	Wed 4/1/20
8	Phase 2 Temp Shoring	4520	SF	150	30 days	Wed 4/1/20	Mon 6/1/20
9	Phase 2 Temp Retaining Wall	140	SF	25	6 days	Mon 6/1/20	Thu 6/11/20
10	Phase 2 Excavation	2900	CY	500	6 days	Thu 6/11/20	Wed 6/24/20
11	Phase 2 RW Drill Shaft	637	LF	40	16 days	Wed 6/24/20	Mon 7/27/20
12	Phase 2 Ret Wall	242	SF	150	2 days	Mon 7/27/20	Wed 7/29/20
13	Phase 2 Bridge Drill Shaft	430	LF	40	11 days	Mon 7/20/20	Tue 8/11/20
14	Phase 2 Bridge Abutment	40	CY	2	20 days	Tue 8/11/20	Thu 9/17/20
15	Phase 2 Drainage Structures	20	CY	1	20 days	Thu 9/17/20	Wed 10/28/20
16	Phase 2 Rock Riprap	300	CY	30	10 days	Wed 10/28/20	Tue 11/17/20
17	Phase 2 Bridge Beams	516	LF	25	21 days	Thu 11/5/20	Thu 12/17/20
18	Phase 2 Bridge Slab, Rail & Approaches	2760	SF	50	55 days	Wed 12/9/20	Mon 3/29/21
19	Phase 2 Roadway Cement Trt Base	525	SY	100	6 days	Wed 3/17/21	Tue 3/30/21
20	Phase 2 Roadway Flex Base	1320	SY	250	6 days	Tue 3/30/21	Mon 4/12/21
21	Phase 2 Roadway Surface	210	TON	200	2 days	Mon 4/12/21	Wed 4/14/21
22	Phase 3 TCP	1	LS	1	1 day	Wed 4/14/21	Thu 4/15/21
23	Phase 3 SW3P	570	LF	500	1 day	Thu 4/15/21	Mon 4/19/21
24	Phase 3 Excavation	2900	CY	500	6 days	Mon 4/19/21	Thu 4/29/21
25	Phase 3 Ret Wall DS	200	LF	40	5 days	Thu 4/29/21	Mon 5/10/21
26	Phase 3 Ret Wall Fascia	764	SF	150	5 days	Mon 5/10/21	Wed 5/19/21
27	Phase 3 Bridge Drill Shaft	344	LF	40	9 days	Mon 5/10/21	Thu 5/27/21
28	Phase 3 Bridge Abutment	34	CY	2	17 days	Thu 5/27/21	Wed 6/30/21
29	Phase 3 Drainage Structures	20	CY	1	20 days	Wed 6/30/21	Mon 8/9/21
30	Phase 3 Rock Riprap	297	CY	30	10 days	Mon 8/9/21	Mon 8/30/21
31	Phase 3 Bridge Beams	391	LF	25	16 days	Wed 8/18/21	Mon 9/20/21
32	Phase 3 Bridge Slab, Rail & Approaches	2700	SF	50	55 days	Thu 9/9/21	Mon 12/27/21
33	Phase 3 Roadway Cement Trt Base	525	SY	100	6 days	Thu 12/16/21	Wed 12/29/21
34	Phase 3 Roadway Flex Base	1320	SY	250	6 days	Wed 12/29/21	Mon 1/10/22
35	Phase 3 Roadway Surface	210	TON	200	2 days	Mon 1/10/22	Thu 1/13/22
36	MBGF, SGTs & Mow Strip	325	LF	30	11 days	Thu 1/13/22	Thu 2/3/22
37	Seeding & Delineation	1	LS	.1	10 days	Thu 2/3/22	Wed 2/23/22
38	Final Clean Up	1	LS	0.5	2 days	Wed 2/23/22	Mon 2/28/22

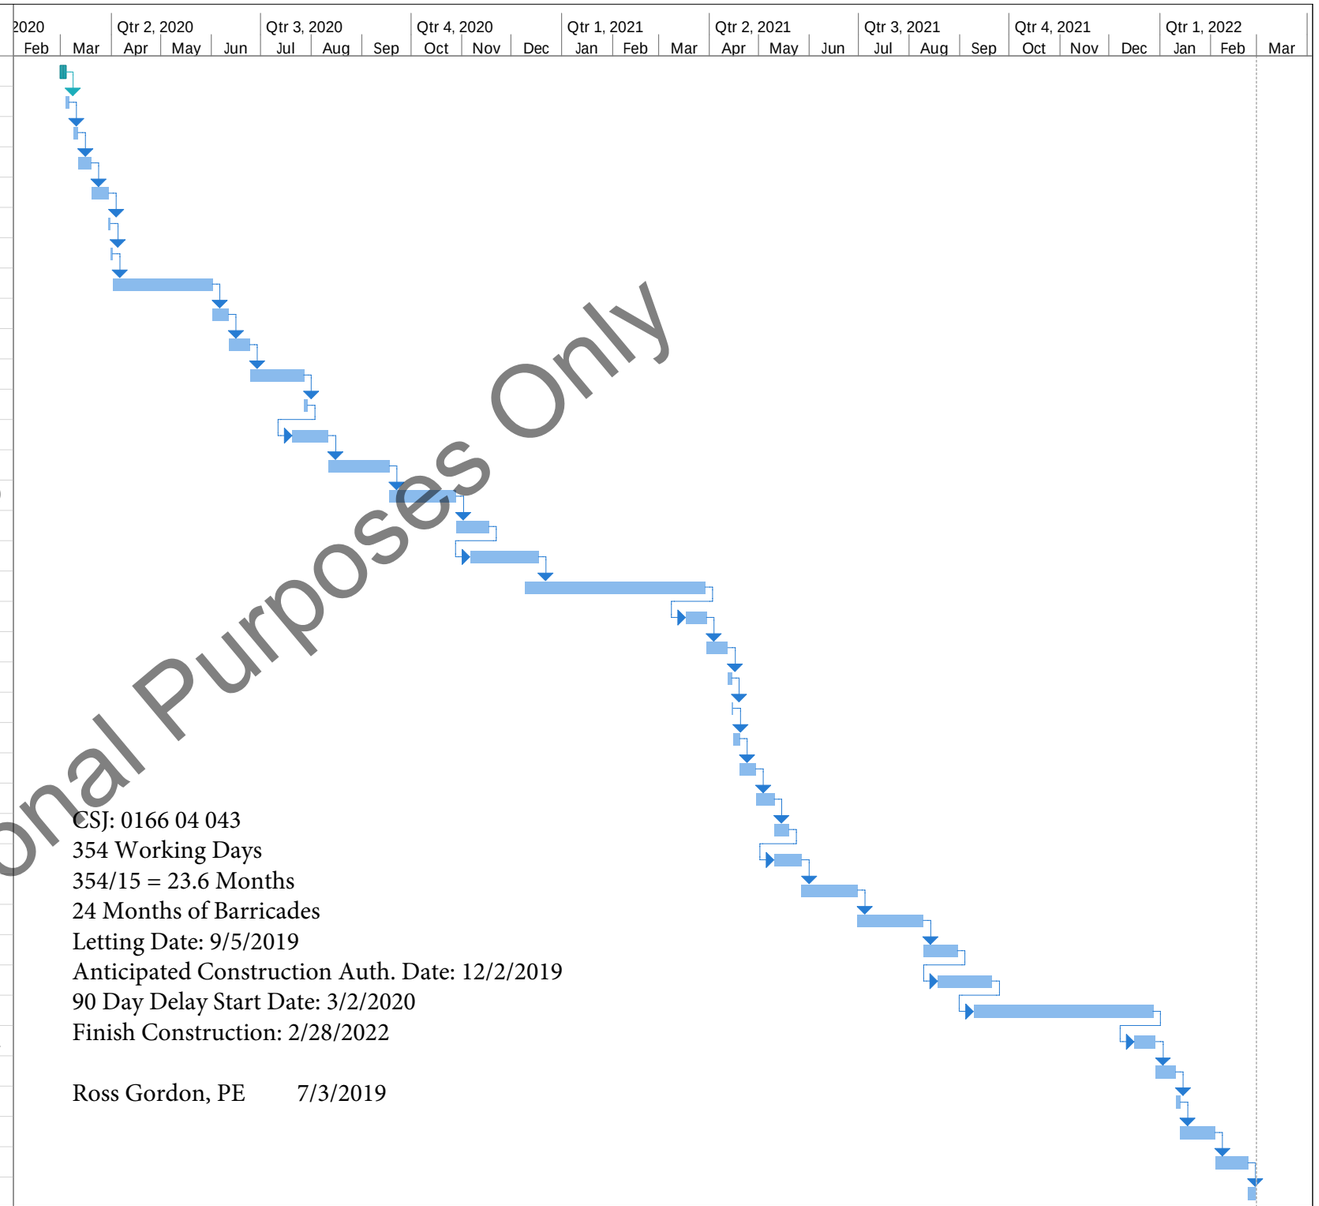

CSJ: 0166 04 043
354 Working Days
354/15 = 23.6 Months
24 Months of Barricades
Letting Date: 9/5/2019
Anticipated Construction Auth. Date: 12/2/2019
90 Day Delay Start Date: 3/2/2020
Finish Construction: 2/28/2022

Ross Gordon, PE 7/3/2019

For Informational Purposes Only

Project: SH75 Contract Time.m
Date: Wed 7/3/19

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
